

Schindler Elevator Corporation
Elevator Power Data

Job Name:	
	Unit(s): 01
	Capacity: 3500 lbs
	Speed: 100 fpm
	Building Voltage: 208 VAC
	Product Code: 460
	Travel: 15 ft0 in

Coordination: All electrical equipment placement and installation shall be coordinated with the Local Schindler Superintendent prior to Schindler manning the jobsite.

Signature Required to Acknowledge & Approve Requirements Outlined Below:

Name: _____

Date: _____

Elevator Equipment Power

(JH): The Elevator Disconnecting means:

- Shall be an enclosed, externally operable, motor circuit switch, shall be listed and lockable in the open position in accordance with NFPA 70.
- Shall be supplied and located in a building utility space outside the hoistway due to the Motor Controller being located in the Elevator Hoistway. One disconnect is required for each elevator. A label on the disconnect is required stating location of the supply side (feeder) overcurrent protection device in accordance with NFPA 70.
- All conductors connecting to Schindler equipment shall be copper; aluminum conductors may be used elsewhere in feeder circuits, as permitted by local electrical codes.
 - a. 208 Volts; 3 Phase; 60 Hz
 - b. Balanced Wye line to line, 3 wire & a Ground (no neutral)
 - c. Must be within +/- 10% of the specified voltage.
 - d. 3% maximum phase to phase fluctuation.
 - e. Cannot be a Delta wiring scheme
 - f. SCCR rating of equipment 5000 Amps. Refer to SCCR section in Appendix
 - g. SCCR rating label required NFPA 70. Refer to SCCR section in Appendix
 - h. Current Consumption by System
 - Accelerating (non-continuous) <3.5 Secs: 29.3 Amps

- Running (non-continuous) < 0.1 Sec Max. Run Time: 26.2 Amps
- i. Elevator Motor Controller Horsepower Demand
 - 10.8
- j. Current Regeneration back to the Building
 - Decelerating (non-continuous) <3.5 Sec: -0.8 Amps
 - Running (non-continuous) < 0.1Sec Max. Run Time: 4.6 Amps
- k. ~~Recommended Fuse Size: Sized by GC (does not account for Voltage drop): [5] Amps~~
 - Maximum Size 70 Amps
 - System Running Current at Constant Speed 26.2 Amps
 - Recommended Receptacle Rating based on fuse size
 - Dual element time delay characteristic recommended
- l. Feeder size based on Secondary Fusing (reference Autotransformer Section above if present) of Transformer or Building Fuse Size (3 ungrounded conductors & an equipment grounding conductor) in accordance with NFPA 70.
- m. Auxiliary dry contact for Evacuation in accordance with NFPA 70.
 - Dry contact closes when Switch turns circuit ON
 - Wiring, in separate conduit, to terminals located in Test and Inspection Panel on Floor 2 located in Controller (LDU).

Note: Shunt Trip Circuit Breaker Required When Sprinklers are Present: The Electrical contractor shall provide a shunt trip circuit breaker for the elevator main line power conductors in order to remove power from elevator controls upon or prior to the application of water from any sprinkler located in any elevator machine room/space, control room/space and hoistway overhead in accordance with ASME A17.1. The shunt trip circuit breaker shall be installed in accordance with NFPA 70 and local regulations.

- Shunt trip shall also have an auxiliary dry contact for Auto-Evacuation when provided as required by NFPA 70.
- Refer to diagram at end of document

(JH1) Non-Fused Disconnect:

- The additional enclosed, externally operable, non-fused motor circuit switch: Shall be listed and lockable open in accordance with NFPA 70
- Shall be supplied and located at the top of the Elevator Hoistway in the space designated on the Layout Drawings and within sight of the motor controller. One switch is required for each elevator. A label on the disconnect is required stating location of (JH) the branch circuit overcurrent protection device- In accordance with NFPA 70 and local regulations.
- All conductors connecting to Schindler equipment shall be copper; aluminum conductors may be used elsewhere in feeder circuits, as permitted by local electrical codes.
 - a. 208 Volts; 3 Phase; 60 Hz
 - b. Feeder size based on fusing size of Elevator Disconnecting Means (JH) (3 ungrounded conductors & an equipment grounding conductor) in accordance with NFPA 70 and local regulations.
 - c. Wire from Motor Circuit Switch to Schindler Equipment

- d. Wire from Motor Circuit Switch to TSU (TSU provided by Schindler in Hoistway)
- e. Feeder size to match incoming feeders to motor circuit switch.
- f. Auxiliary dry contact for Auto-Evacuation (when provided) in accordance with NFPA 70.
- g. Dry contact closes when Switch turns circuit ON
- h. Wiring, in separate conduit, to terminals located in the Test and Inspection Panel located on Floor 2 the Controller (LDU) Floor

Receptacles:

GFCI (Ground-Fault Circuit Interrupter) type receptacles shall be provided in all elevator pits and machinery/control spaces inside the hoistway. All receptacles in elevator machine rooms, machinery spaces, control rooms and control spaces outside the hoistway shall be provided with ground-fault circuit interrupter protection in accordance with NFPA 70.

Lighting:

Elevator Machine Rooms, control spaces, and test and inspection panel location
Requiring Lighting: ASME A17.1. requires the minimum level of illumination measured at the floor to be 19fc.

- See layouts for details of size and location requiring lighting.

Elevator Pits Required Lighting: ASME A17.1 requires the minimum level of illumination measured at the pit floor to be 10fc. The location shall be determined after coordination with the elevator contractor so that the light fixture(s) are located out of the way of all elevator equipment.

- See layouts for details of size and location requiring lighting.

Fire Service Access elevators:

Schindler provides a 24VDC output to activate a relay for hoistway lighting. Relays and hoistway lighting is provided by others. Minimum illumination is 5fc.

Receptacles and Switches:

Sump Pump Receptacles: A receptacle for a sump pump shall be required in all elevator pits for the elevator pit if provided with a sump pump. A single receptacle supplying a permanently installed sump pump shall not require ground-fault circuit-interrupter protection in accordance with NFPA 70.

Elevator Machine and Control Rooms Light Switch Requirement: Light switches shall be required in all elevator machine and control rooms adjacent to the jamb side of the machine room entry door- where practicable in accordance with NFPA 70 and ASME A17.1.

Elevator Machinery Space Light Switch Requirement:

- (overhead) at the point of entry in accordance with NFPA 70 and ASME A17.1
- Provided at point of entry on strike side (lock-jamb) of door at top floor.
- See layouts for location detail.

Elevator Pit Light Switch Requirement: The pit switch shall be a minimum of 18 inches above the elevator lowest landing doorsill and adjacent to (not behind) the pit access ladder in accordance with NFPA 70 and ASME A17.1.

- See layouts for location detail.

Grounding:

An equipment grounding conductor shall be supplied from the elevator main line disconnecting means and controller to the MCC and building ground-in accordance with NFPA 70 Article 250.

Branch Circuits:

Car Lighting Disconnect:

120 Volts, 1-Phase, 60 Hertz, 15 Amps

A separate branch circuit shall supply the car lights, receptacle(s), auxiliary lighting power source, and ventilation on each elevator car. The disconnecting means shall be an enclosed, externally operable, fused switch or circuit breaker that is lockable open and shall be located in the machine room or control room for that elevator car. Where there is no machine room or control room, the disconnecting means shall be located in the building utility space outside the hoistway that is readily accessible to only qualified persons.

- Wiring from Car Lighting Disconnect to the Test and Inspection Panel (LDU).

2 Separate Circuits for Elevator Pit:

The elevator pit shall have a separate branch circuit supplying pit lighting and receptacle(s) and shall be permitted to have another for the pit sump pump when one is provided in accordance with NFPA 70 (Does not interface with Schindler equipment).

- See layouts for location detail.

2 Separate Branch Circuits for Machinery Space Lighting and Outlets in the Elevator Overhead:

The overhead machinery space shall have separate branch circuits supplying the machinery space lighting and receptacles in accordance with NFPA 70 (Does not interface with Schindler equipment).

Inspection and Test panel:

where provided shall be lit by permanently installed electric lighting with a level of illumination of at least 200 lx (19 fc) at the floor level. A switch placed inside or close to the enclosure shall control lighting of the enclosure in accordance with ASME A17.1 and NFPA 70.

Emergency Phone and Data Line: Conduit shall be provided by electrical contractor in all elevator machine rooms to the elevator controller. Electrical contractor shall

provide electrical conduit for both the emergency elevator phone and required data line to the elevator machine room, to the elevator controller, and terminated on the elevator controller with coordination from the elevator contractor. The building shall provide:

1. Communication requirements for two-way audio device (If Schindler Ahead phone function is not being installed)
 - a. Wiring of Phoneline to the Test and Inspection Panel (LDU) or RCC cabinet
 - An analog telephone line, one per elevator group, shall be provided by the building. Line shall be capable of receiving incoming and making outgoing calls
 - Phone line which is provided from a native digital source must be able to work with modem modulated devices (e.g. fax machines).
 - b. If Schindler Ahead is not used, and another 3rd party cellular gateway is utilized, it is the responsibility of the building to provide a system compatible with the in-car phone for reliability and quality
 - c. Building shall arrange for live staffing (automated answer system is prohibited) to respond to call for help from the elevator car. If the call is not acknowledged within 45S, the call shall be automatically directed to an alternate on- or off- site location.
 - d. Where the elevator rise is 18m (60ft) or more, an additional telephone/phone line shall be provided within the building at a location accessible by emergency personnel. This phone line shall support equipment that is capable of two-way analog communications with each elevator car (via each car's Inspection and Test Panel) individually and overriding communications between the elevator car and locations outside of the building.
2. Communication requirements for two-way visual communication device (If Schindler Ahead phone function is not being installed or Visual Alarm Module (VAM) or Visual Communications Panel (VCS) is provided)
 - a. A generic network with a regular ISP Modem
 - b. Where the elevator rise is 18m (60 ft) or more, or seismic operation (Counterweight Derailment) is provided according to A17.1-2016 or later requirements, A single RJ45 wired Ethernet communications circuit shall be provided by the building.
 - c. Where the elevator rise is below 18m (60ft), separately wired RJ45 Ethernet communications circuits, one per elevator group, shall be provided by the building.
 - d. The recommended minimum upload speed is 0.5Mb/s per elevator connected to the communication system.
 - e. The communications circuit shall originate at the Elevator Control Visual Alarm Box, part of the two-way visual communication device designed by Schindler and terminate at the building WAN internet equipment.
 - f. This internet connection is required to have an un-interrupted power supply for a duration of 4 hours to allow the Visual Communication Device to function if building power is lost.

GFCI type receptacles, light fixtures and light switches:

are required in elevator overhead machinery spaces located in the hoistway that requires "full body entry" (as defined by elevator code).

are required in machinery spaces outside the hoistway.

- See layouts for location detail.

Electrical Component NFPA Clearances: Clearances around all electrical equipment in the elevator machine room shall comply with NFPA 70 electrical clearances requirements. The electrician's work and equipment placement shall be coordinated with the elevator contractor's equipment placement.

Electrical Piping Runs: All electrical piping runs provided by the electrical contractor and elevator contractor to the elevator equipment shall be run overhead or in a manner which does not restrict access to and around any equipment.

Fire Control Panel Smoke Detector relays:
(Primary, Secondary & Fire Hat) mounted within 3 ft. of Inspection and Test Panel (LDU) or control cabinet (RCC). Additional Smoke Detector relays in addition to the three (3) mentioned may be necessary depending on job site conditions. To be coordinated with Schindler.

- Wiring from Smoke Detector Relays to Inspection & Test Panel (LDU)
- NC, dry contacts required

Heat Detector (if applicable):

Located within 2 ft of hoistway sprinkler head

Wiring from Heat Detector to Shunt Trip Breaker (if applicable; does not interface with Schindler equipment unless in Detroit)

Installation Power:

- a. Temporary power supply for installation work. (220 V, 1 phase, 50/60 Hz, 20 Amp power supply, GFCI protected w/Time-Delay fuse);

This requires coordination with Schindler to determine which is applicable

Heat Emissions:

Hoistway – 2193 BTU/Hr

Hallway – (LDU – Inspection & Test panel only) – 600 BTU/Hr

Appendix

SCCR Information to include in this document

The SCCR rating of elevator equipment is 5000 Amps, contractor to ensure that the available fault current of the building supply at the service switch does not exceed this value (Per NFPA 70). Contractor to include a label

(Please see figure 2-Sample Label Example) that identifies the Max Available Fault Current onto Disconnect: ** See note 1 of Figure 1-SCCR Diagram. In addition, we require a hard copy of the manufacturers Fuse Chart and rating verifying the SCCR meets requirements.

Per NFPA 70, the service switch should be legibly marked with Apparent RMS Symmetrical fault current supplying the Elevator Equipment. ** See note 3 of Figure 1-SCCR Diagram.

Local Electrical Contractor must provide building SCCR Current calculations as well as Fuse Chart and rating to prove compliance with 5KA elevator equipment rating for the supplied fuse.

** See note 2 of Figure 1-SCCR Diagram.

From Building Electrical Distribution Panel

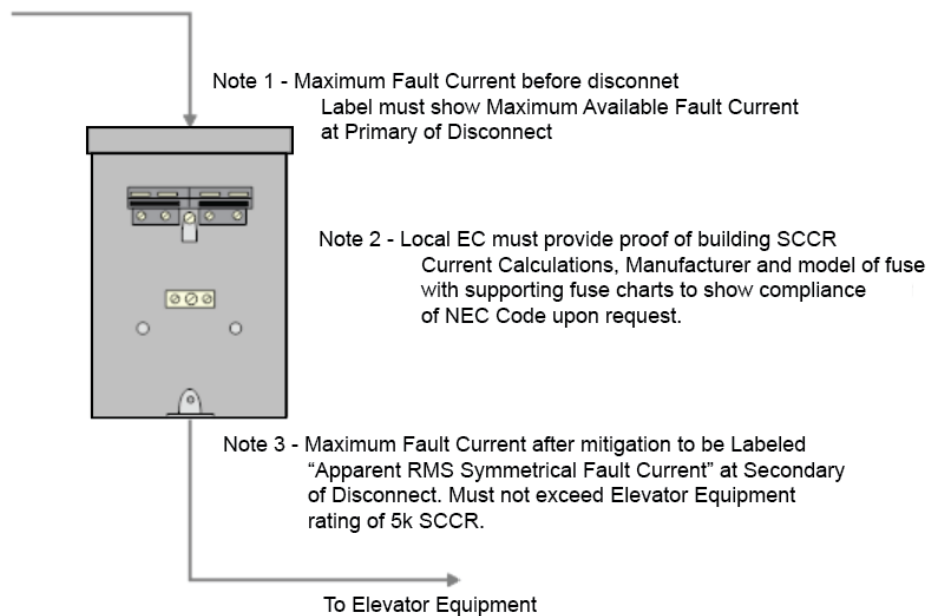


Figure 1- SCCR Labelling Diagram

Maximum available fault current _____A
Electrical Firm / Electrician: _____
Date: _____

Figure 2: Sample Label

SHUNT TRIP CONTROL WIRING DIAGRAM

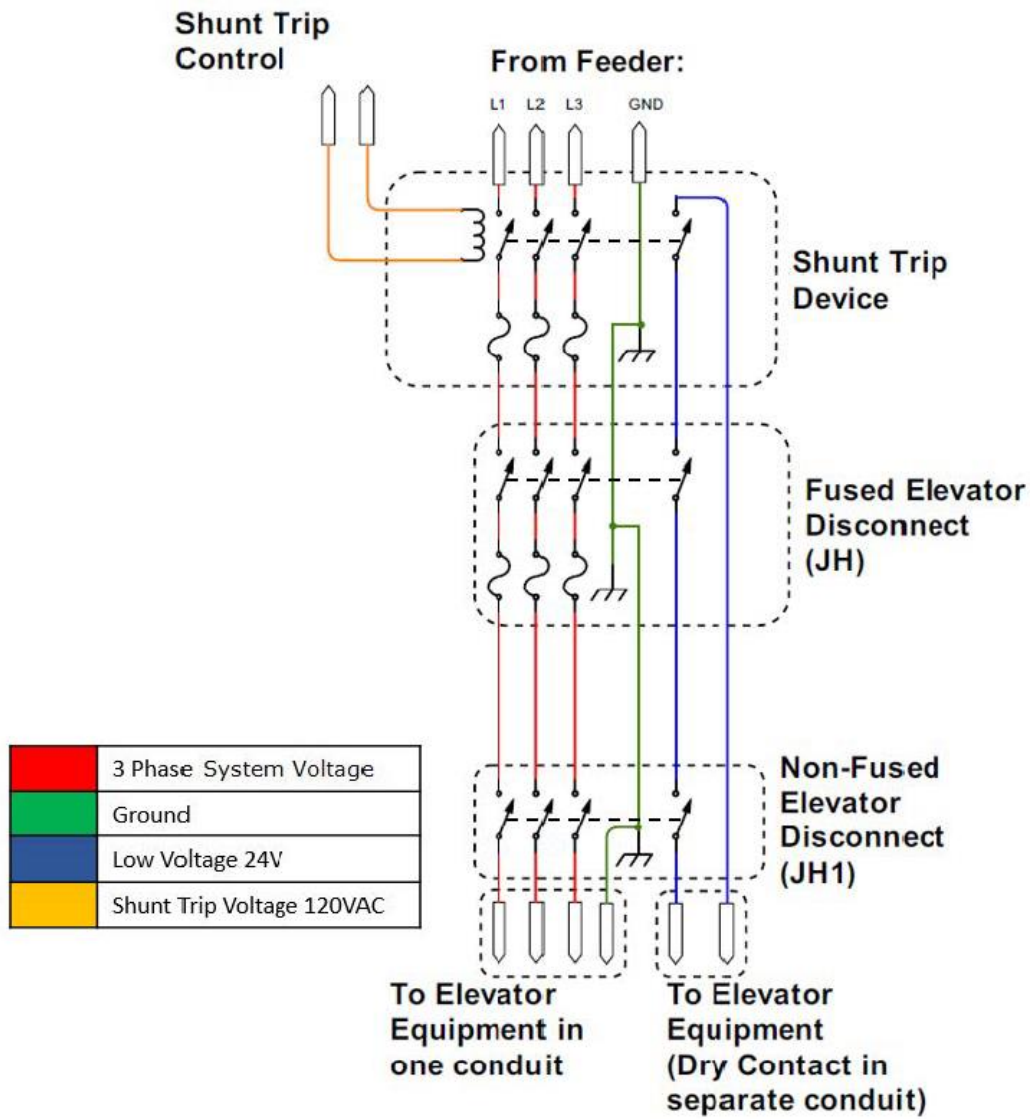


Figure 3: Shunt Trip Wiring


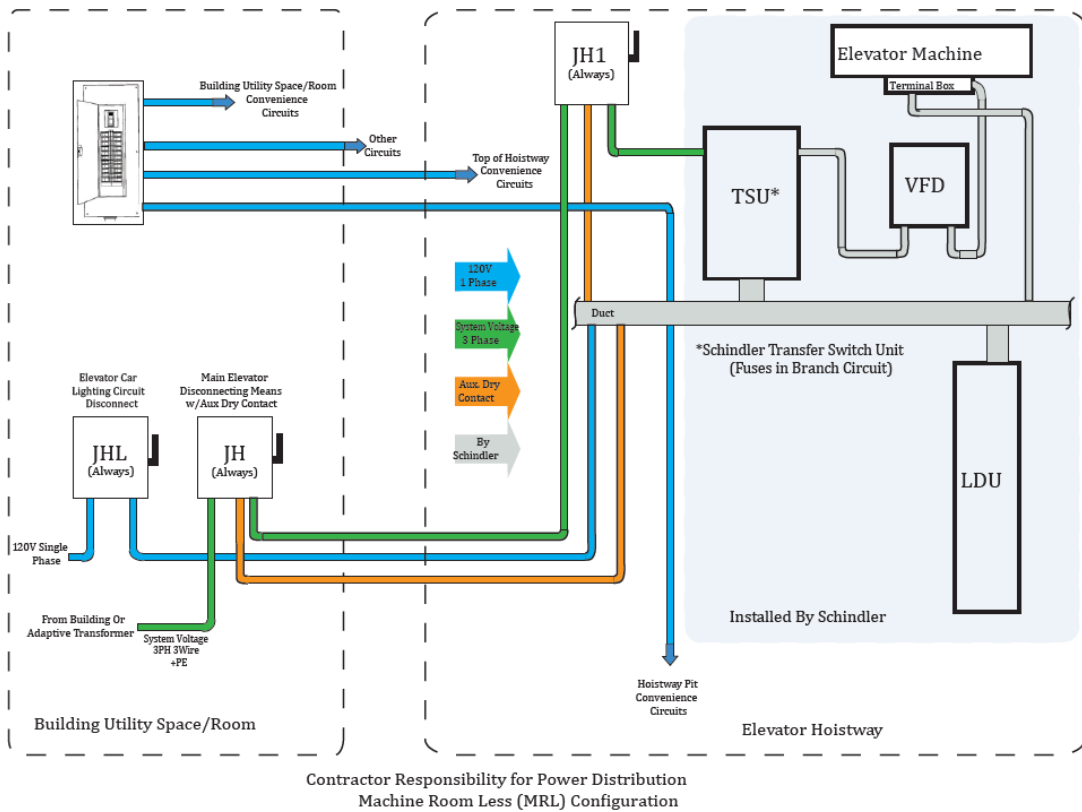


Figure 5.
See Layouts for exact location of equipment in Overhead and pit.

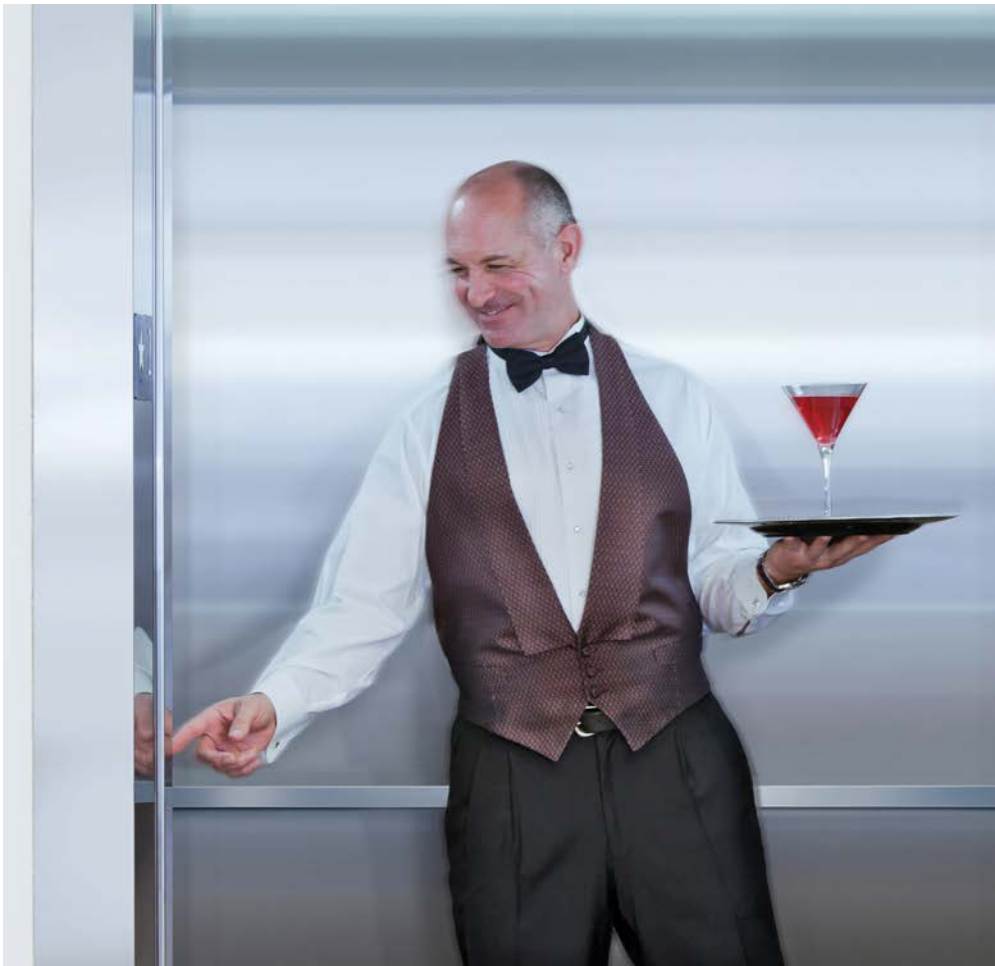

Schindler 3300 XL

Space-saving traction technology.
Expanded capabilities. Eco-friendly.

We Elevate



Schindler

us.schindler.com



The Schindler 3300 XL elevator for passenger and service applications in low- to mid-rise buildings

» Space optimization

Machine room-less design provides more usable building space and roomier cars for greater passenger comfort.

» Class A characteristics

Elevate your building with tall cars, entrances and center opening doors on a 4,000 lb. general purpose configuration; accommodating IBC 2009 and greater stretchers.

» Understated elegance

Stylish yet refined, the Schindler 3300 XL seamlessly integrates the beauty of Italian design with the precision of Swiss engineering, all while being able to accommodate as much as 1,350 lbs. in additional weight.*

» Superior performance

Quieter, smoother traction technology combined with expanded service capacity and range. Passengers will notice the smoother ride. Building owners will appreciate the increased capabilities.

» Eco-friendly

Designed with sustainability and energy efficiency in mind, the Schindler 3300 XL is up to 60% more efficient than a hydraulic elevator. Power Factor 1 regenerative drive comes standard.

*Applies to front-opening 4,500 lbs service configuration with tall cars and entrances.

The Schindler 3300 XL — when specifications require more. More room. More speed. More lift.

The Schindler 3300 XL was developed to serve the low- and mid-rise building market with larger cars and more entrance and deco options. Capacities include 3,500 lbs. general purpose, 4,000 lbs. general purpose/hospital service, 4,500 lbs. hospital service, and 5,000 lbs. hospital service/AIA.

The world's most enlightened elevator

The Schindler 3300 traction elevator is recognized globally as the smartest choice for low- to mid-rise commercial and residential buildings.

To meet the broader needs of commercial, hospital and service applications, the Schindler 3300 line has been expanded to include a XL line with additional capabilities:

- Larger cars
- Faster travel speeds
- Greater load capacity
- Smoother rides
- Less noise
- MRL configuration
- Lower energy consumption
- More design and aesthetic options

More room. More usable space.

As architects around the world can attest, the Schindler 3300 XL is designed to maximize the square footage of the car interior. And, while delivering larger cars and greater load capacities, the Schindler 3300 XL is still a machine room-less system*.

This MRL design reduces building interfaces, saves valuable usable space and increases efficiency.

Feels, sounds and looks better

In addition to being roomier, our cars are constructed using high-quality, high-strength materials with sound dampening and isolating materials making them more stable, comfortable and quieter.


Thanks to our suspension traction media (STM), the Schindler 3300 XL glides smoothly and quietly through your building. Elevator movements go virtually unnoticed — which will certainly be appreciated by occupants of your building.

Our standard design palettes are anything but “standard”. We can provide exceptional looks, while keeping lead times and costs down. From stainless steel to a distinctive collection of attractive laminates or powder coat paint, your design choices are easier than ever before.

Designed for our passengers and our planet

With automatic evacuation available, we've elevated our focus on safety. In the event of a power failure, you will be taken safely to the next floor. We're also setting a new standard in conservation. The Schindler 3300 XL is economical in its use of energy, which contributes to lower operating costs and a smaller carbon footprint.

*Please consult your local sales representative for local code MRL details.

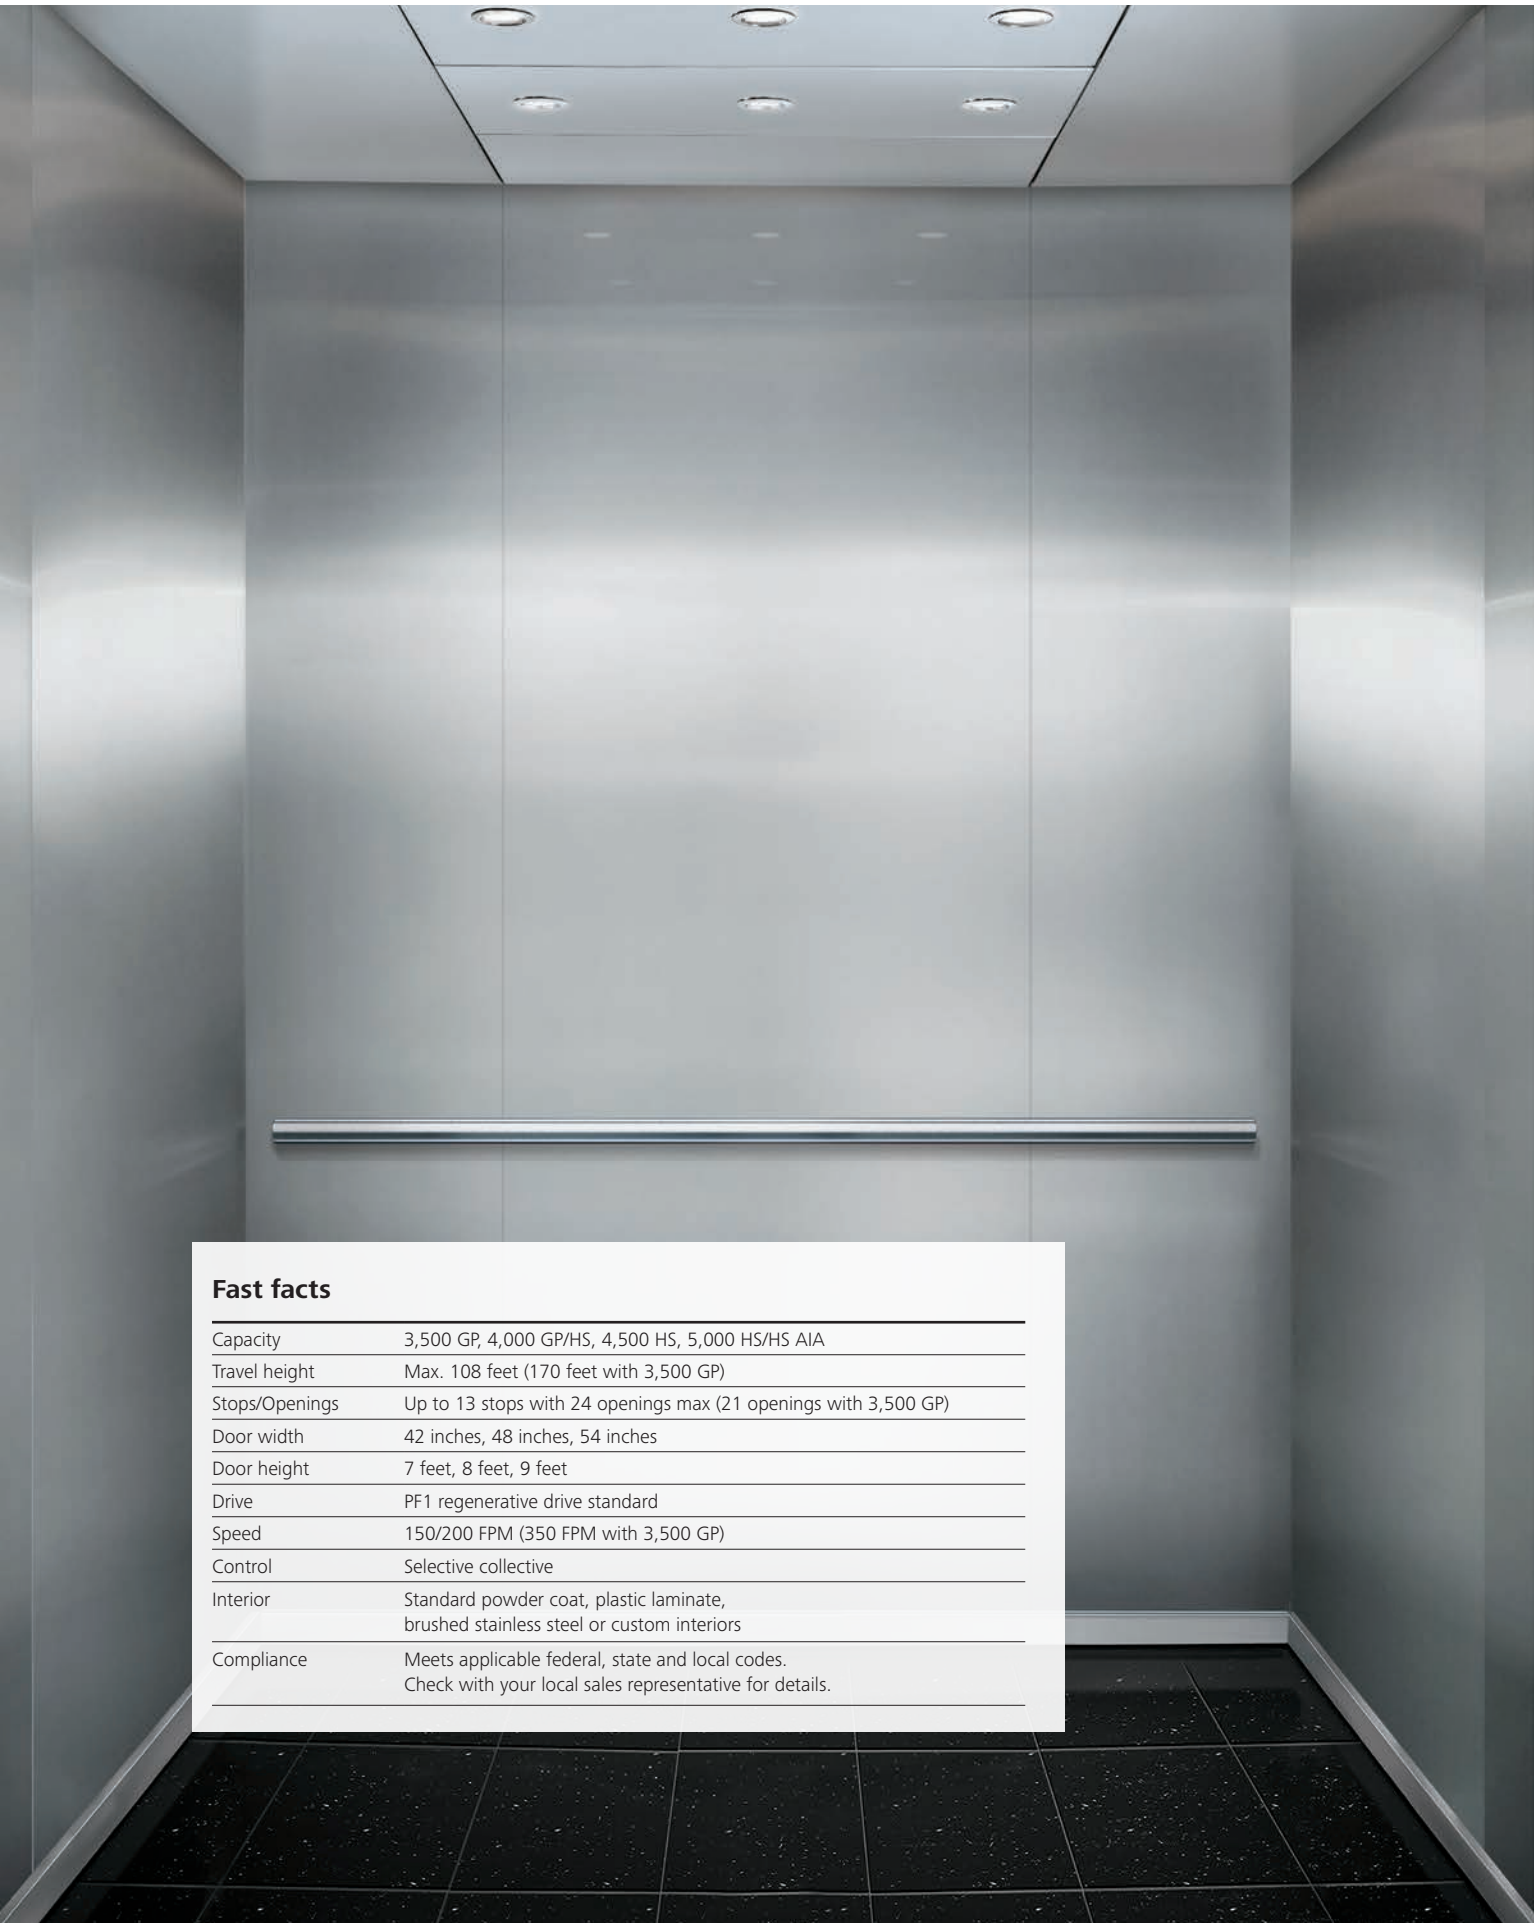

Fast facts

Capacity	3,500 GP, 4,000 GP/HS, 4,500 HS, 5,000 HS/HS AIA
Travel height	Max. 108 feet (170 feet with 3,500 GP)
Stops/Openings	Up to 13 stops with 24 openings max (21 openings with 3,500 GP)
Door width	42 inches, 48 inches, 54 inches
Door height	7 feet, 8 feet, 9 feet
Drive	PF1 regenerative drive standard
Speed	150/200 FPM (350 FPM with 3,500 GP)
Control	Selective collective
Interior	Standard powder coat, plastic laminate, brushed stainless steel or custom interiors
Compliance	Meets applicable federal, state and local codes. Check with your local sales representative for details.


Space optimization

The Schindler 3300 XL delivers more space where you need it, when you need it, with capacities ranging from 3,500 lbs. to 5,000 lbs.

Car sizing options for passenger, hospital, and service applications

With cars up to 10 feet tall, 7'-4³/₁₆" wide and 9'-1¹/₄" deep, the Schindler 3300 XL is adaptable to meet an expanded range of applications including commercial, residential, hospitality, healthcare, and service.

In general passenger service, roomier cars significantly enhance rider comfort. In hospital, hospitality and service applications, larger cars easily accommodate stretchers, luggage carts and other material handling equipment.

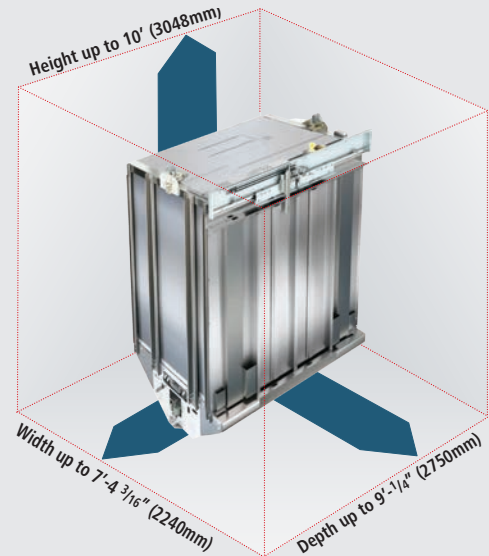

MRL design saves valuable building space

The reduced space requirements for technical equipment and components deliver significant advantages:

- Fits into a standard hoistway
- Requires no machine room or control closet
- Needs minimal hoistway overhead
- Eliminates unsightly roof structures

Space-saving measures include:

- Small, powerful drive located in the hoistway overhead
- High-strength, flexible suspension traction media (STM)
- Compact inspection and test panels in the top landing hoistway door jamb or a jamb up to 74' away from the top landing
- Control distributed throughout the system



Class A characteristics

Affordable Class A characteristics include center opening doors, stretcher compliance, and 4,000 GP cars along with multi-car bank symmetry.



You'll find our processes are streamlined, simple, and quick – from planning to installation.

Planning

The Schindler 3300 XL requires no machine room, which means only the elevator hoistway has to be designed. Standardized plans mean less planning, making the process simple and efficient.

Ordering

Every 3300 XL easily accommodates an IBC 2009 or later stretcher, including the 4,000 lb. GP with center opening doors. Since there are no complicated specifications, you can quickly and effortlessly find the product that fits your needs.

Delivery

We help minimize workspace clutter by delivering the Schindler 3300 XL complete, in a single shipment, just in time for its installation.

Installation

Whether it's a single unit or a symmetrical multi car bank with up to four units, the elevator installs quickly. No cranes or scaffoldings are required. Depending on the configuration, the system can be ready in as little as a few weeks.

Superior performance


Traction technology delivers noticeably quieter and smoother service. Passengers will notice the better ride. Building owners will appreciate the increased reliability and efficiency.

Current: steel cables

Steel cables used in elevators are relatively inelastic, requiring a traction sheave diameter of at least 12 inches plus a motor with drive gears large enough to match. A system that requires more space and is intrinsically inefficient.

Future: Suspension Traction Media (STM)

Suspension traction media are more flexible, can use a traction pulley diameter as small as 4.25 inches and require a much smaller motor. A space and energy saving design.

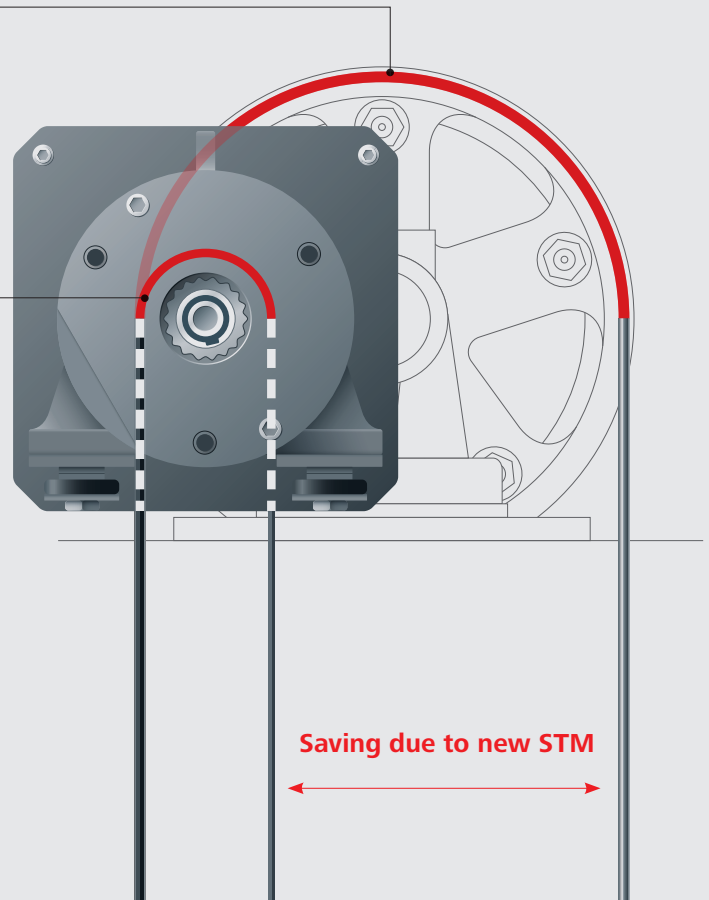

Drive system

The Schindler 3300 XL requires a small hoist machine and inverter. This saves more space compared to previous drive systems; it is installed directly in the overhead and does not require a separate machine room. The system stops the car with precision. Car and landing floor line up very accurately to ensure that passengers get in and out safely. The system is economical in energy consumption and causes minimal noise due to the material of the suspension traction media (STM). The regenerative drive further increases efficiency and can deliver energy back to the building.

Suspension Traction Media (STM)

The STM consists of strong surface-coated steel wire ropes sheathed in a non-circular polyurethane jacket. They replace conventional steel cables, weigh less, require less space and run quieter. Thanks to the STM, there is room for the machine and drive directly in an even smaller elevator hoistway.

Inspection and test panel


The inspection and test panel is built directly into a standard doorframe at the top landing, or in a jamb up to 74' from the top landing. This highly functional solution simplifies elevator installation, provides practical handling, and saves space. The Schindler 3300 XL does not require a space-consuming machine room or control closet. However, some jurisdictions still require such space. In those areas, contact your local Schindler sales representative for a room or closet solution.

Doors

Doors are equipped with a frequency-controlled drive for fast and reliable operations. Two-speed side-opening doors opening to the left or right, as well as single-speed center-opening doors, are available.


Car

Technology does not take much space in the Schindler 3300 XL. This benefit allows relatively small hoistways to be utilized while providing a larger car interior.

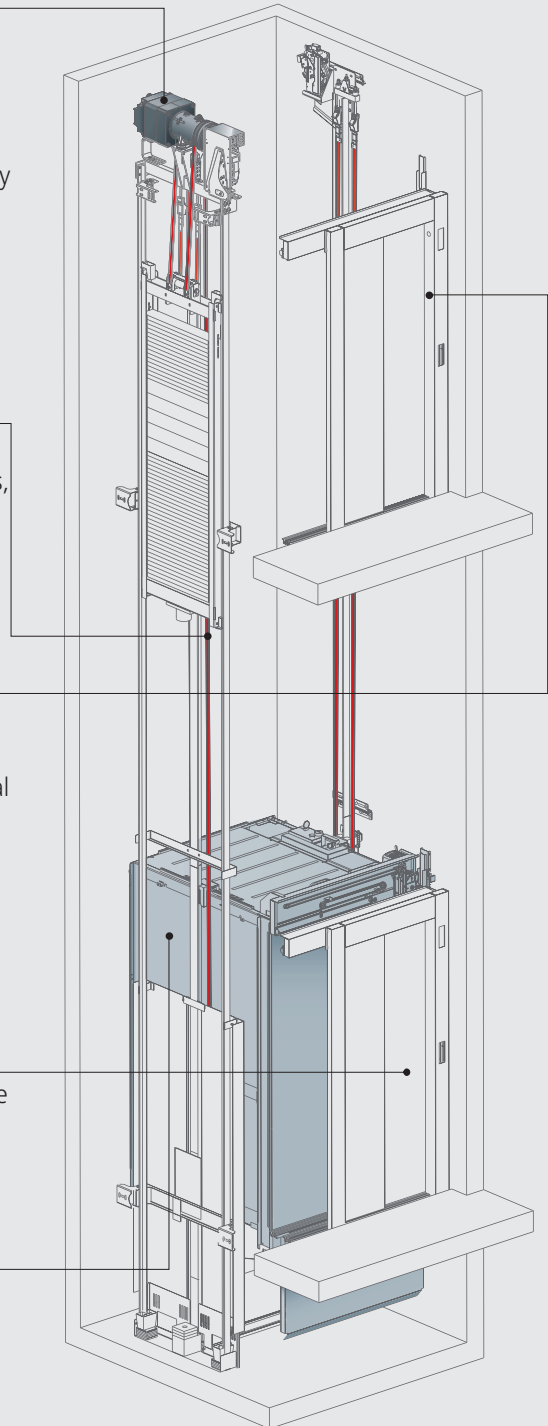


Understated elegance

Make a grand entrance. Begin your design with a choice of stainless steel or 11 durable powder coat finishes. Entrances and landing doors are available in center-opening or side-opening configurations, with left-hand or right-hand openings.




Distinctive brushed stainless steel cab is an optional upgrade

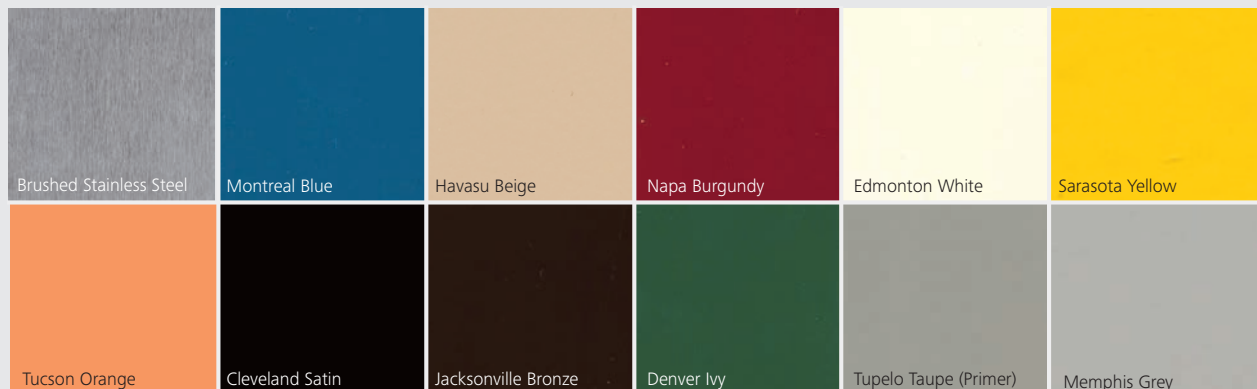

Our hall fixtures are composed of stainless steel and tempered safety glass panels, back-printed in white for a modern look. Please refer to our fixtures brochure for additional options, including vandal-resistant.



Combination hall lantern and position indicator




Hall pushbuttons



Car lantern



Vandal-resistant combination hall lantern and position indicator



Vandal-resistant hall pushbuttons




Car operating panel*



Vandal-resistant Car operating panel



Round handrail - (shown with optional returned ends)




Flat handrail

The unique ceiling design comes standard in brushed stainless steel with classic LED round spot downlights. Optional line light fixtures can enhance your elevator design.



Ceiling lighting - standard LED round spot downlights**

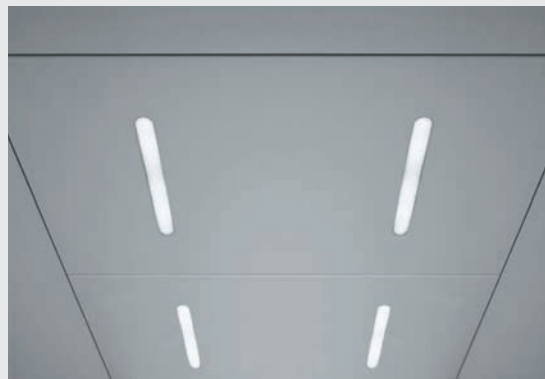

Ceiling lighting - line light option**

Note: The car specifications, options and colors in this brochure are representative only and are subject to change.

Sample shown may vary from the original in color and material.

*Car operating panel available as half height non flush mounted, or full height flush mounted. Vandal-resistant option available on full height car operating panels.

**Quantity of LED round spot downlights or line light fixtures depends on the elevator size/configuration.

Add personality to your elevator


Car walls are available in stainless steel, powder coat, a choice of plastic laminates, or other options including hung panels. More options are available in addition to the standards shown. If your vision requires something unique, custom car options are also available. Consult your sales representative for details.



Distinctive stainless steel cab is an optional upgrade

Powder coated painted walls

Fresh, flashy and multifaceted

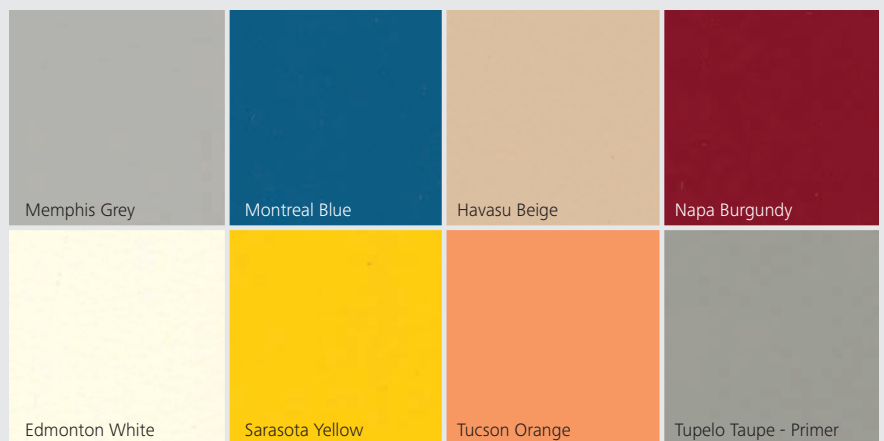

Powder coat colors

Warm, distinguished and genuine




Laminates with subtle, wavelike design

Laminated walls

Clean, cool and cutting edge



Mesa Mercury Glass

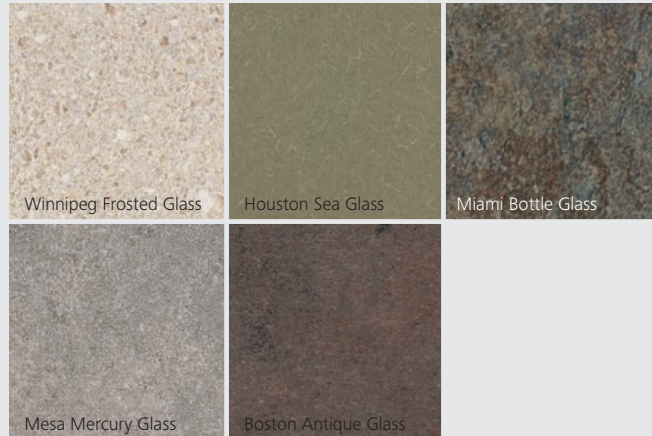

These laminates provide a clean, cutting-edge aesthetic

Steely, sophisticated and elegant



Toronto Grey



Laminates with subtle, monochromatic patterns

Rich, natural and classic




Baltimore Cherry



Rich, wood-grain color laminates

Eco-friendly

Up To



More Efficient
Than Hydraulic
Elevators



Schindler is a member of the U.S. Green Building Council and supports the LEED® Green Building Rating System. Designed with sustainability and energy efficiency in mind.

Drive

- Power Factor 1 regenerative drive comes standard
- Compact, lightweight and durable design
- Gearless machine saves energy and avoids power loss
- Stable start uses energy more efficiently and reduces electric costs
- Frequency converter with standby power mode safely returns elevator to nearest floor during power outage

Cab

- Car lighting uses energy-efficient LED lamps
- Central guiding system reduces friction and energy consumption
- Door drive with standby mode uses less electricity
- Larger cabs are also stronger and lighter weight

Control

- When not in use, car lights automatically switch to standby mode
- Car panel and floor indicators use low power LEDs
- Multi-bus control architecture reduces cabling and material waste
- Smart controls provide more efficient passenger transportation

The perfect combination of people-centered design and technology

The features and components of the Schindler 3300 XL are designed to enhance the rider experience, improve safety, and minimize downtime. Schindler predictive maintenance anticipates difficulties before they occur, and allows rapid response to service calls. From the low-energy multiprocessor controls to the stylish, stainless steel fixtures, you'll find the latest technological advances.



Seamless connectivity

Made for today. Ready for the future.

With Schindler Ahead, we turn data into results for customers and passengers.

Schindler Ahead is a cloud platform, powered by GE Predix. Using 4G connectivity, this closed-loop digital platform allows your connected equipment to become part of the Building Internet of Things (IoT). Secure, automated data collection and real-time analytics provide insights that allow for predictive maintenance, equipment visibility, maximized uptime and more accurate capital planning. Building owners, facilities managers and passengers can have the relevant information they need, when they need it.

To learn more about Schindler Ahead, visit www.schindler.com/ahead-us.

Key benefits of Schindler Ahead



- High reliability and uptime improves overall building performance
 - Insights about component lifetime allow for better mid-term planning of repairs and modernizations
 - Complete digital documentation of equipment portfolio
 - 24/7 digital emergency service
 - Increased building value by connecting to Internet of Things
 - Cost-saving solutions with service guarantees and removal of phone line
- High reliability and uptime with fast reaction times, thanks to predictive maintenance
 - Real-time information on equipment status and performance
 - Full transparency on status of maintenance activities, due to push notifications via app, text, or email
- Reduced wait times and increased reliability lead to potential improvements in the passenger experience
 - Regular status updates about equipment and maintenance work via the app, text, or email
 - Increased convenience thanks to interactive and personalized information

SchindlerPlan.com

Elevator and escalator design in minutes



Schindler Plan is an easy-to-use online planning tool that makes it simple to configure your elevator or escalator in minutes. Good elevator or escalator design plays a critical role in the quality of life and work in multi-story buildings. Schindler Plan was developed to enable accurate escalator or elevator preparation early in a project's life cycle.

Schindler 3300XL Machine Room-Less (MRL) Traction Elevator with PF1 Regenerative Drive

Capacity 3,500 – 5,000 lbs.

Passengers 21 – 31

Speed 150 – 200 FPM (350 FPM with 3,500 GP)


Travel height Up to 108' and 13 stops, 24 openings
(170 feet and 21 openings with 3,500 lbs. GP)

Cab height 7'-9", 9', 10' (7'-9" shown)


Door height 7', 8', 9' (7' shown)⁸

Hoistways

Front opening

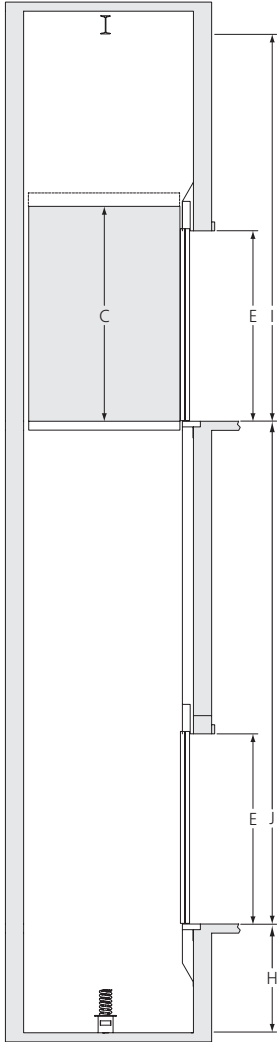


Front/rear opening

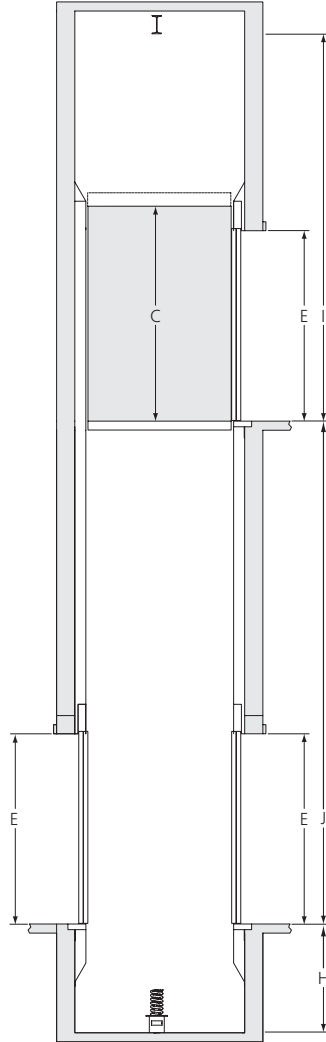


Hatch plans:

General Purpose


Front opening single-speed center opening (SSCO)

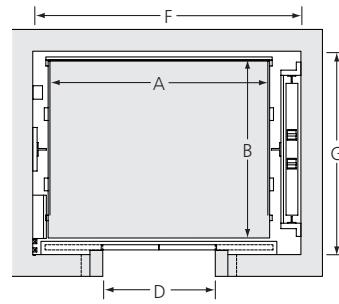


Front/rear opening single-speed center opening (SSCO)

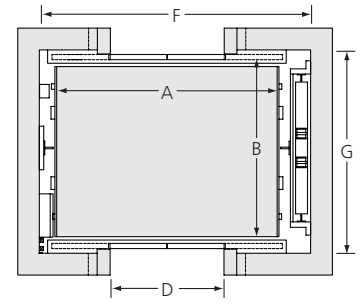

Front opening two-speed¹ left opening (2SSO)

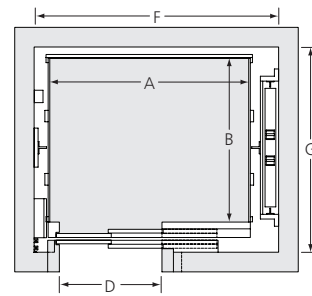


Front/rear opening two-speed¹ left opening (2SSO)

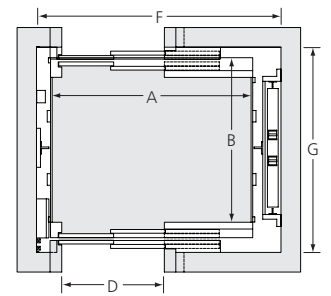


Hospital/Service

Front opening two-speed¹ left opening (2SSO)

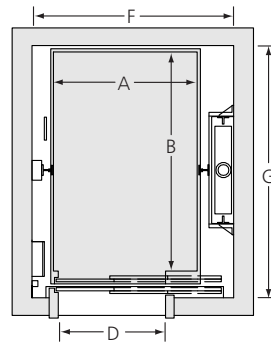

Front/rear opening two-speed¹ left opening (2SSO)

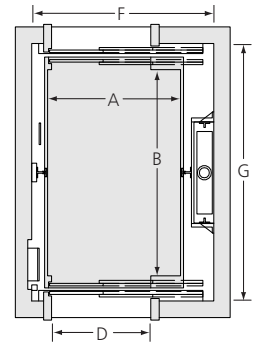

Abbreviations:

A Cab width

B Cab depth

C Car height

D Door width

E Door height⁸

F Hoistway width

G Hoistway depth

H Pit depth



I Clear overhead

SSCO Single speed center opening door

2SSO Two speed side opening door¹

General Purpose, Hospital/Service, HS AIA

Specifications and Layout Data

Load Capacity lbs (kg)	Cab Width	Cab Depth	Door Type	Door Width	Hoistway Width	Hoistway Depth		Speed fpm (m/s)	Height ft-in (mm)	Clear Overhead ⁴		Pit Depth		
							Front only ft-in (mm)			Front & Rear ft-in (mm)			PU Buffer Minimum ⁹ ft-in (mm)	Spring Buffer Minimum ft-in (mm)
General Purpose														
3,500 (1,590)	6'-4 9/16" (1945)	5'-6 15/16" (1700)	SSCO	3'-6" (1067)	8'-4" (2540)	6'-11 1/16" (2110)	7'-4 1/2" (2248)	150 (0.76)		7'-9" (2362)	12'-7" ⁹ (3835)	12'-11 1/4" (3942)	4'-0" ⁹ (1219)	4'-0" (1219)
	6'-4 9/16" (1945)	5'-6 15/16" (1700)	2SSO	3'-6" (1067)	8'-4" (2540)	6'-11 1/16" (2110)	7'-7 11/16" (2328)			9'-0" (2743)	13'-10" ⁹ (4216)	14'-2 1/4" (4323)	4'-0" ⁹ (1219)	4'-0" (1219)
4,000 (1,815)	7'-4 3/16" (2240)	5'-7" (1700)	SSCO	4'-0" (1219)	9'-4" (2843)	6'-8 1/8" (2035)	7'-4 3/16" (2240)			10'-0" (3048)	14'-10" ⁹ (4521)	15'-2 1/4" (4628)	4'-0" ⁹ (1219)	4'-0" (1219)
Hospital Service														
4,000 (1,815)	5'-4 1/4" (1632)	7'-8 1/2" (2350)	2SSO	4'-0" (1219)	7'-4" (2235)	8'-11 5/16" (2725)	9'-9" (2970)	200 (1.02)		7'-9" (2362)	12'-8" ⁹ (3858)	13'-4 3/16" (4068)	4'-0" ⁹ (1219)	4'-1 5/16" (1219)
4,500 (2,040)	5'-4 1/4" (1632)	8'-2 1/2" (2500)	2SSO	4'-0" (1219)	7'-4" (2235)	9'-5 3/16" (2875)	10'-2 7/8" (3120)			9'-0" (2743)	13'-11" ⁹ (4239)	14'-7 3/16" (4449)	4'-0" ⁹ (1219)	4'-1 5/16" (1219)
5,000 (2,270)	5'-4 1/4" (1632)	8'-8 5/16" (2650)	2SSO	4'-0" (1219)	7'-4" (2235)	9'-11 1/8" (3025)	10'-8 3/4" (3270)			10'-0" (3048)	14'-11" ⁹ (4544)	15'-7 3/16" (4754)	4'-0" ⁹ (1219)	4'-1 5/16" (1219)
5,000 AIA (2,270)	5'-8 7/8" (1750)	9'-0 1/4" (2750)	2SSO	4'-0" (1219)	7'-8 5/8" (2353)	10'-3 1/16" (3125)	11'-0 11/16" (3370)	3,500 lbs only		Oil Buffer ft-in (mm)		Oil Buffer ft-in (mm)		
										7'-9" (2362)	13'-4" (4060)	5'-0" (1524)		
										9'-0" (2743)	14'-7 3/16" (4449)	5'-0" (1524)		
								350 (1.78)		10'-0" (3048)	15'-7 3/16" (4754)	5'-0" (1524)		

Door height: 7', 8', 9' ⁸

Door height: 7', 8', 9' ⁸

Notes:

- 2SSO doors are available with right or left openings. Optional hand (diagonal) door layout complies with stretcher access if needed. Please contact your local Schindler Sales Representative for more information.
- Up to four car group operation is available. Please consult with your local Schindler Sales Representative for more information.
- For areas in seismic zone 2 or greater, provide additional 2" (50 mm) to the hoistway width.
- Clear overhead is defined as from the lowest point below any obstruction such as: hoist beam(s), building beams, or roof structure.
- Where permitted by code, no control closet is required. A 3-phase and 110v disconnect must be located in both the hoistway overhead and a location in the building outside of the hoistway. The latter is not required to be an elevator-dedicated space.
- Schindler recommends an additional 2" hoistway width to the minimums above, for non-seismic regions, and an additional 4" for seismic regions.
- Cab heights available are 7' 9", 8', or 9'. Subtract 4" from these dimensions to underside of canopy.
- Door heights available are 7', 8', or 9', except for 3,500 lb. configuration, where door height is 7' only.
- PU buffer requires a local code review. Please contact your local Schindler Sales Representative for additional PU buffer information.
- These dimensions are for information only and cannot be used for construction purposes without Schindler confirmation. Confirm with your local Schindler Sales Representative.



Schindler – We Elevate

For more information, including the location of the Schindler office nearest you, please visit:

U.S. Headquarters. Morristown, New Jersey
Tel. [REDACTED]
www.us.schindler.com

Canada Headquarters. Toronto, Ontario
Tel. [REDACTED]
www.ca.schindler.com

We Elevate



Schindler has received renewal to ISO 9001 and [REDACTED] certificates.



Schindler prints with vegetable-based ink on paper containing post-consumer waste fiber.
© Schindler Elevator Corporation

WORK BY OTHERS

INSTALLATION WORK SHALL BE PERFORMED DURING REGULAR WORKING HOURS OF REGULAR WORKING DAYS AFTER HOISTWAY(S) AND MACHINE/CONTROL ROOM(S) HAVE BEEN PROPERLY PREPARED AS DESCRIBED IN THE FOLLOWING ITEMS. ALL ITEMS MUST BE PERFORMED OR FURNISHED AT NO COST TO SCHINDLER ELEVATOR CORPORATION ("SCHINDLER") BY THE OWNER OR GENERAL CONTRACTOR OR THEIR AGENTS IN ACCORDANCE WITH ALL GOVERNING CODES. THE PRICE AND INSTALLATION SCHEDULE OF SCHINDLER IS BASED ON THESE JOB-SITE CONDITIONS EXISTING AT THE BEGINNING AND DURING THE INSTALLATION OF THE ELEVATOR EQUIPMENT.

ALL WORK MUST BE PERFORMED PER THE LATEST APPLICABLE REVISION OF THE NATIONAL (ASME A17.1 OR CSA B44) AND/OR LOCAL CODES.

1.

CLEAR, PLUMB, HOISTWAY WITH VARIATIONS NOT TO EXCEED +25MM (+1") -0MM (-0") WITHIN THE FIRST 30.5M (100FT). TOLERANCE MAY INCREASE +0.8MM (1/32") FOR EACH ADDITIONAL 3.05M (10FT) UP TO A MAXIMUM OF +50MM (2"). PIT FLOOR TO BE DRY, LEVEL, FREE OF BUMPS AND DEBRIS. HOISTWAY ENCLOSURE TO BE FIRE RATED PER NATIONAL CODE REQUIREMENTS AND APPLICABLE BUILDING CODES (RULE 2.1.1). HOISTWAY, PIT, AND OVERHEAD DIMENSIONS TO BE AS SPECIFIED ON SCHINDLER FINAL LAYOUT DRAWING.
2.

ACCEPTABLE MATERIAL UNLOADING AREA WITHIN 30.5M (100FT) OF HOISTWAY WITH "ROLLABLE" ACCESS (PLANKED OR PAVED) OR UNINTERRUPTED USE OF A CRANE OR FORKLIFT AND OPERATOR AT NO COST TO SCHINDLER. DRY AND ENCLOSED STORAGE AREA OF ADEQUATE SIZE FOR ELEVATOR MATERIALS NEAR HOISTWAY. ANY WARRANTIES PROVIDED BY SCHINDLER FOR ELEVATOR EQUIPMENT ARE NULL AND VOID IF EQUIPMENT IS STORED IN A MANNER THAT DOES NOT COMPLY WITH THE REQUIREMENTS AS DEFINED ABOVE.
3.

POWER FOR CONSTRUCTION ADJACENT TO HOISTWAYS AND MACHINE/CONTROL ROOMS (110/220 VOLT, SINGLE PHASE, FOR WELDERS AND HOISTS) AND SUFFICIENT 3-PHASE POWER TO RUN ELEVATOR(S) AT THE SAME TIME. REFER TO SCHINDLER POWER SUPPLY DATA SHEET. TO MEET THE DATE UPON WHICH THE ELEVATORS ARE TO BE TURNED OVER, THE POWER FOR CONSTRUCTION AND PERMANENT 3-PHASE POWER MUST BE INSTALLED AND AVAILABLE PRIOR TO THE START OF ELEVATOR INSTALLATION.
4.

ALL WORK AREAS, INCLUDING HOISTWAY AND PIT, CLEAR OF DEBRIS. MAINTAIN MINIMUM TEMPERATURE OF 13°C (55°F). ADEQUATE WORK AREA IN FRONT OF GROUND FLOOR ENTRANCE REQUIRED. PROPER LIGHTING OF WORK AREAS.
5.

75° BEVEL GUARDS ON ALL PROJECTIONS, RECESSES OR SETBACKS OVER 100MM (4"), EXCEPT ON SIDE USED FOR LOADING/UNLOADING.
6.

PROVIDE VENTING OF THE HOISTWAY PER NATIONAL CODE REQUIREMENTS AND APPLICABLE BUILDING CODES (RULE 2.1.4). WHEN IBC COMPLIANCE IS REQUIRED, AN INDEPENDENT AC OR VENTING SYSTEM FOR THE ELEVATOR SYSTEM IS REQUIRED.
7.

DRIED-IN HOISTWAY(S) AND MACHINE/CONTROL ROOM(S).
8.

CLEAR, FLAT, VERTICAL OR HORIZONTAL SURFACES FOR MOUNTING RAIL BRACKETS AT EACH FLOOR, IN OVERHEAD, AND INTERMEDIATE LEVELS (IF REQUIRED) IN THE SAME VERTICAL PLANE AS THE CLEAR HOISTWAY LINE. THIS INCLUDES DIVIDER BEAMS BETWEEN CARS FOR MULTIPLE ELEVATORS IN A COMMON HOISTWAY. RAIL BRACKET SUPPORTS SHALL NOT INTRUDE INTO THE CLEAR HOISTWAY LINE. RAIL BRACKET SUPPORTS AND DIVIDER BEAMS IN THE OVERHEAD TO BE LOCATED APPROXIMATELY 610MM (24") BELOW THE ROOF OR MACHINE ROOM SLAB. SUPPLY VERTICAL FLAT PLATES ON WHICH TO MOUNT CAR RAIL BRACKETS IF GUSSET PLATES OBSCURE BEAM WEBS, SUCH AS IN WIND BRACING FRAMES. IF APPLICABLE, INTERMEDIATE BRACKET SUPPORTS BETWEEN FLOOR(S) AND IN THE OVERHEAD AREA MAY BE REQUIRED. REFER TO SCHINDLER FINAL LAYOUT DRAWINGS FOR MAXIMUM BRACKET SPACING AND ACTUAL SUPPORT LOCATIONS.
9.

FOR MASONRY BLOCK HOISTWAY CONSTRUCTION, SCHINDLER WILL PROVIDE RAIL BRACKET INSERTS FOR INSTALLATION BY OTHERS, LOCATED IN ACCORDANCE WITH THE SCHINDLER FINAL LAYOUT DRAWINGS. WHERE INSERTS ARE NOT USED, HOLLOW MASONRY BLOCKS ARE NOT ACCEPTABLE FOR BRACKET FASTENING. PROVIDE 125MM (5") CONCRETE BELT AROUND HOISTWAY OR OTHER ACCEPTABLE SUPPORT AT EACH FLOOR, IN OVERHEAD, AND INTERMEDIATE LEVELS (IF REQUIRED).
10.

BLOCKOUT/CUTOUT THROUGH WALL AS REQUIRED, TO ACCOMMODATE HALL BUTTON BOXES, SIGNAL FIXTURES, AND HATCH DUCT. PROVIDE FOR ANY REPAIRS SUCH AS GROUTING, PATCHING, PAINTING, OR FIRE PROOFING.
11.

FOR NON-MASONRY HOISTWAY CONSTRUCTION WITH FLOOR HEIGHTS EXCEEDING 4.5M (15FT), STRUCTURAL SUPPORT AT 2.4M (8FT) TO 4.5M (15FT) ABOVE FINISHED FLOOR LEVEL FOR ENTRANCE STRUT ANGLE ATTACHMENT.
12.

FOR MASONRY HOISTWAY WALLS AT ENTRANCES, PROVIDE ROUGH OPENING OF 203MM (8") ON EACH SIDE AND 203MM (8") ON TOP OF CLEAR OPENING FOR INSTALLATION OF DOORFRAMES AND SILLS. FOR DRYWALL HOISTWAY WALLS AT ENTRANCES, WALLS ARE TO BE BUILT AFTER DOORFRAMES AND SILLS ARE SET IN PLACE.
13.

GROUTING AROUND ENTRANCE FRAMES AND FINISHED FLOOR AND GROUT TO SILL LINE AFTER INSTALLATION OF ENTRANCE.
14.

CONSTRUCTION BARRICADES (PER OSHA REQUIREMENTS) EITHER OUTSIDE OF ELEVATOR HOISTWAY(S) OR BETWEEN ELEVATORS INSIDE OF HOISTWAY(S) AS REQUIRED. BARRICADES TO BE FREESTANDING AND REMOVABLE, LOCATED AT EACH HOISTWAY OPENING AT EACH FLOOR. BARRICADES SHALL BE ERECTED, MAINTAINED, AND REMOVED BY OTHERS.
- PROTECTION FROM FALLS

A.

AS REQUIRED BY THE OCCUPATIONAL SAFETY AND HEALTH ADMINISTRATION (OSHA) 1926.502 B) (1-3) A FREESTANDING REMOVABLE BARRICADE AT EACH HOISTWAY OPENING AT EACH FLOOR. BARRICADES SHALL BE 42" HIGH, WITH MID-RAIL AND KICK BOARD, AND WITHSTAND 200 LBS. OF VERTICAL AND HORIZONTAL PRESSURE.

B.

AS REQUIRED BY THE OCCUPATIONAL SAFETY AND HEALTH ADMINISTRATION (OSHA) OSHA 1926.502(d) HOISTWAY PROTECTION FROM FALLING DEBRIS AND OTHER TRADES MATERIALS BY EITHER:

1.

8 FOOT SCREENING/MESH IN FRONT OF ALL ELEVATOR ENTRANCES

2.

SECURED/CONTROLLED ACCESS TO ALL ELEVATOR LOBBIES (LOCK AND KEY) WITH POSTED NOTICE "ONLY ELEVATOR PERSONNEL BEYOND THIS PROTECTION"
15.

DRY PIT REINFORCED TO SUSTAIN VERTICAL FORCES FROM RAILS AND IMPACT LOADS ON BUFFERS (RULE 2.2.2). CAR BUFFER IMPACT LOADS AS CALCULATED (RULE 8.2.3).
16.

ADEQUATE SEALING AND WATERPROOFING OF PIT. EFFECTIVE PREVENTION OF PIT EXPOSURE TO STORM WATER OR GROUND WATER.
17.

WHERE THERE IS A DIFFERENCE IN LEVEL BETWEEN THE FLOORS OF ADJACENT PITS, A METAL GUARD SHALL BE INSTALLED NOT LESS THAN 2000 MM (79") ABOVE THE LEVEL OF THE HIGHER PIT FLOOR (RULE 2.2.3.1). WHERE THE DIFFERENCE IN LEVEL IS 600 MM (24") OR LESS, A STANDARD RAILING CONFORMING TO RULE 2.10.2 SHALL BE PERMITTED (RULE 2.2.3.2).
18.

DRAINS & SUMPS IN ELEVATOR PITS, WHERE PROVIDED, SHALL COMPLY WITH THE APPLICABLE PLUMBING CODE, AND THEY SHALL BE PROVIDED WITH A POSITIVE MEANS TO PREVENT WATER, GASES AND ODORS FROM ENTERING THE HOISTWAY. SUMPS AND SUMP PUMPS IN PITS, WHERE PROVIDED, SHALL BE COVERED. THE COVER SHALL BE SECURED AND LEVEL WITH THE PIT FLOOR (RULES 2.2.2.4 AND 2.2.2.6) AND SHOULD BE LOCATED TO CLEAR ELEVATOR EQUIPMENT (CANNOT BE CONNECTED DIRECTLY TO STORM DRAIN OR SEWER).
19.

GFCI CONVENIENCE OUTLET AND LIGHT FIXTURE WITH GUARD IN PIT (NATIONAL ELECTRICAL CODE (NFPA 70 RULE 620-85) OR (CSA C22.1-02 SECTION 38-085)). MINIMUM LIGHTING TO BE 100 LUX (10FC) (RULE 2.2.5).
20.

PIT LADDER FOR EACH ELEVATOR IN COMPLIANCE WITH RULE 2.2.4.2. NEAREST POINT OF THE LADDER SHALL BE WITHIN 975MM (39"), MEASURED HORIZONTALLY FROM THE MEANS TO UNLOCK THE EGRESS DOOR FROM THE PIT. THE LADDER SHALL EXTEND NOT LESS THAN 1200MM (48") ABOVE THE SILL OF THE ACCESS DOOR. RUNGS OR CLEATS TO BE NON-SLIP AND SHALL BE SPACED 300MM (12") ON CENTER AND 400MM (16") WIDE (SEE RULE 2.2.4.2 FOR EXCEPTION WHEN UNAVOIDABLE OBSTRUCTIONS ARE ENCOUNTERED). LOCATE PER SCHINDLER FINAL LAYOUT DRAWINGS AND DRAWING DS823. ALL WALK-IN PITS MUST FOLLOW THE REQUIREMENTS OF RULE 2.2.4.5.
21.

GFCI CONVENIENCE OUTLET AND TELEPHONE OUTLET LOCATED IN MACHINE/CONTROL ROOM FOR EACH ELEVATOR (NATIONAL ELECTRICAL CODE (NFPA 70 RULE 620-85) OR (CSA C22.1-02 SECTION 38-085)). DEDICATED ANALOG TELEPHONE LINE CAPABLE OF OUTGOING AND INCOMING CALLS FOR EMERGENCY PHONE SYSTEM (RULES 2.27.1.1 & 2.27.1.2) AND SCHINDLER REMOTE MONITORING (SRM).
22.

MAIN POWER CIRCUIT

A.

JH: A DEDICATED LOCKABLE WALL-MOUNTED OR RECESSED SELF LOCKING PANEL WITH A FUSED DISCONNECT SWITCH OR CIRCUIT BREAKER (WHERE PERMITTED) SUITABLE FOR 3-PHASE POWER FOR THE ELEVATOR CONTROL, LOCATED IN A) THE BUILDING COMMON ELECTRICAL UTILITY ROOM, OR B) A BUILDING SERVICE CORRIDOR, OR C) ON / IN A WALL WITHIN SIGHT OF THE ELEVATOR INSPECTION AND TEST PANEL. DISCONNECT SWITCH OR BREAKER MUST ALSO HAVE AN AUXILIARY (DRY) CONTACT THAT IS POSITIVELY DRIVEN AND OPENS WHEN THE BREAKER OR SWITCH IS OPENED.

B.

JH1: ONLY WHEN MOTOR CONTROLLER IS LOCATED IN HOISTWAY: AN ADDITIONAL LOCKABLE WALL-MOUNTED NON-FUSED DISCONNECT SWITCH IN THE HOISTWAY, TO BE LOCATED ADJACENT TO THE MOTOR CONTROLLER. THIS DISCONNECT MUST ALSO A) BE LOCKABLE IN THE CLOSED POSITION WITH A LOCKING MECHANISM THAT CANNOT BE REMOVED FROM THE DEVICE AND B) HAVE AN AUXILIARY (DRY) CONTACT THAT IS POSITIVELY DRIVEN AND OPENS WHEN THE SWITCH IS OPENED. (SEE ALSO NFPA70 REQ. 620.51(C)(1) OR CSA C22.1 REQ. 38-051(6)).

C.

POWER WIRING FROM JHL TO THE CORRESPONDING INSPECTION AND TEST PANEL.

D.

OTHER SINGLE-PHASE FUSED DISCONNECT SWITCHES OR CIRCUIT BREAKERS FOR FUNCTIONS RELATED TO THE ELEVATOR, INCLUDING BUT NOT LIMITED TO POWER FOR RECEPTACLES, LIGHTING, REMOTE MONITORING EQUIPMENT, SEISMIC EQUIPMENT, AND PIT PUMPS, LOCATED ADJACENT TO THE 3-PHASE PANEL OR WITHIN THE 3-PHASE PANEL.

E.

WIRING FROM "OTHER" DISCONNECTS TO RECEPTACLES/LIGHTING DEVICES AT THE DESTINATIONS (PIT, TOP HOISTWAY, MACHINERY/CONTROL SPACES, CONTROL ROOMS, MONITORING STATIONS, ETC.)
23.

GENERAL

THE DEDICATED PANELS OUTSIDE THE HOISTWAY IDENTIFIED ABOVE AND THEIR LOCATION MUST BE IN AN AREA READILY ACCESSIBLE TO QUALIFIED/AUTHORIZED PERSONS (NFPA 70 REQ. 620.51(C)) OR / (CSA 22.1 REQ. 38-051(5)). ACCESS TO EACH DISCONNECT PANEL MUST REQUIRE A GROUP 2 KEY (ASME A17.1/CSA B44 REQ. 8.1.3). THE DISCONNECTS MAY ALSO BE LOCATED WITHOUT PANELS IN A GROUP 2 KEY SECURED ROOM IDENTIFIED AND DEDICATED FOR THE ELEVATOR APPARATUS ONLY. LOCATE AND MARK THE PANELS AND DISCONNECTS WITH APPROPRIATE SIGNAGE, (NFPA 70 REQ. 620-51 THROUGH 620-55) OR (CSA C22.1 REQ. 38-051 THROUGH 38-055). EACH DISCONNECT OR BREAKER ABOVE MUST BE CAPABLE OF BEING LOCKED IN THE OPEN POSITION WITH A LOCKING APPARATUS (EXCLUDING LOCK ITSELF) THAT CANNOT BE REMOVED FROM THE DEVICES OR PANEL(S).

24.

OTHER EQUIPMENT/REQUIREMENTS:

A.

FOR THE MAIN POWER CIRCUIT ONLY:

1.

A 3-PHASE TRANSFORMER MAY BE SUPPLIED TO PROVIDE THE REQUIRED MOTOR CONTROLLER VOLTAGE IF NOT DIRECTLY AVAILABLE WITHIN THE BUILDING. WHEN SUPPLIED, IT IS PREFERABLE TO BE LOCATED IN A COMMON ELECTRICAL ROOM WITH OTHER BUILDING ELECTRICAL APPARATUS. SEE SCHINDLER POWER SUPPLY DATA SHEET.

2.

A LOCAL DISCONNECTING MEANS MUST BE PROVIDED IN THE FEEDER TO THIS TRANSFORMER (NFPA70-11 REQ. 450.14) OR (CSA C22.1-12 REQ. 26-250). WHEN THE JH DISCONNECT IS NOT LOCATED WITHIN SIGHT OF THE TRANSFORMER, AN ADDITIONAL (TRANSFORMER) DISCONNECT LOCATED WITHIN SIGHT OF THE TRANSFORMER SHALL BE PROVIDED BY THE BUILDING. THE INSTALLATION OF A TRANSFORMER DISCONNECT DOES NOT ELIMINATE THE NEED FOR THE JH DISCONNECT.

B.

FOR ALL POWER CIRCUITS

1.

SPRINKLERS SHALL BE LOCATED AT THE TOP AND BOTTOM OF THE HOISTWAY WHEN REQUIRED BY THE LOCALLY ADOPTED EDITION OF NFPA 13.

2.

IN US JURISDICTIONS ONLY, WHEN A SPRINKLER HEAD IS LOCATED IN THE HOISTWAY, THE BUILDING SHALL PROVIDE SHUNT TRIP ACTIVATION OF A) JH, THE MAIN DISCONNECT OR B) THE FEED TO THE MAIN DISCONNECT, TRIGGERED BY CONTACTS OF THE FIRE RECALL INITIATING DEVICES (AS DEFINED BY NFPA). THESE DEVICES, LOCATED IN THE HOISTWAY OR OTHER DISCONNECT LOCATION, SHALL PROVIDE INDEPENDENT DISCONNECTION OF ELECTRICAL POWER TO BOTH MAIN AND AUXILIARY POWER CIRCUITS PRIOR TO SPRINKLER ACTIVATION (ASME A17.1-2007/CSA B44-07 RULE 2.8.3.3. AND/OR LOCAL CODE).

3.

SHUNT TRIP, IF PROVIDED, MUST ALSO HAVE AN AUXILIARY CONTACT THAT FUNCTIONS THE SAME AS THOSE IN THE JH AND JH1 DISCONNECTS.

C.

FOR COMMUNICATIONS CIRCUITS

1.

AN ANALOG TELEPHONE LINE, ONE PER ELEVATOR, SHALL BE PROVIDED. LINE SHALL BE CAPABLE OF RECEIVING INCOMING AND MAKING OUTGOING CALLS. TELEPHONE LINE SHALL ORIGINATE AT THE INSPECTION AND TEST PANEL DESIGNATED BY SCHINDLER AND TERMINATE AT THE BUILDING PHONE SYSTEM.

2.

WHERE THE ELEVATOR RISE IS 18 M (60 FT) OR MORE, AN ADDITIONAL TELEPHONE / PHONE LINE SHALL BE PROVIDED WITHIN THE BUILDING AT A LOCATION ACCESSIBLE BY EMERGENCY PERSONNEL. THIS PHONE LINE SHALL SUPPORT EQUIPMENT THAT IS CAPABLE OF TWO-WAY ANALOG COMMUNICATIONS WITH EACH ELEVATOR CAR VIA EACH CAR'S INSPECTION AND TEST PANEL, INDIVIDUALLY AND OVERRIDING COMMUNICATIONS BETWEEN THE ELEVATOR CAR AND LOCATIONS OUTSIDE OF THE BUILDING.

25.

A LOCKABLE, 13 1/2" X 15 1/2" X 3 1/2" (MINIMUM), METAL CABINET WITH GROUP-1 KEY TO HOUSE REQUIRED ELECTRICAL SCHEMATICS AND MAINTENANCE HISTORY DOCUMENTS. SHALL BE WALL MOUNTED, ADJACENT TO THE DISCONNECT SWITCH, BY OTHERS, AT THE TOP LANDING. THE SUPPLIER, LOCATION AND MOUNTING OF THE CABINET SHALL BE COORDINATED WITH SCHINDLER.

26.

PROVIDE SUITABLE FEEDER AND BRANCH WIRING CIRCUITS FROM THE BUILDING SERVICE TO THE CONTROLLER, INCLUDING MAIN LINE SWITCH, FOR SIGNAL SYSTEMS, POWER OPERATED DOORS, CAR LIGHTING AND CONVENIENCE OUTLETS. SEE SCHINDLER POWER SUPPLY DATA SHEET.

27.

PROVIDE EMERGENCY POWER TRANSFER SWITCH AND POWER CHANGE PENDING SIGNALS AS REQUIRED TO MASTER CONTROL.

28.

LIGHTING, VENTILATION, AND HEATING OF MACHINE/CONTROL ROOM, CONTROL SPACE AND MACHINERY SPACE (RULE 2.7.9)(A17.1 RULE 2.7.5; IBC 2006 SECTION 3006.2). MINIMUM LIGHTING TO BE 200 LUX (19FC). A SWITCH PLACED ADJACENT TO THE ENCLOSURE SHALL CONTROL LIGHTING FOR THE JAMB MOUNTED INSPECTION & TEST PANEL. MACHINE/CONTROL ROOM OR CONTROL SPACE TEMPERATURE TO BE MAINTAINED BETWEEN 5°C (41°F) AND 40°C (104°F) WITH LESS THAN 95% NON-CONDENSING HUMIDITY. INSPECTION AND TEST PANEL FLOOR LANDING MIN. 0°C (32°F) AND MAX 40°C (104°F) WITH LESS THAN 95% NON-CONDENSING HUMIDITY. SEE SCHINDLER POWER SUPPLY DATA SHEET FOR HEAT EMISSIONS.

29.

HOIST BEAMS, TRAP DOORS, AND OTHER MEANS OF ACCESS TO MACHINERY SPACE OF ADEQUATE SIZE FOR MAINTENANCE AND EQUIPMENT REMOVAL (RULES 2.7.3.4 AND 2.9.3.3). HOIST BEAMS IN EACH SHAFT LOCATED AND LOAD RATED PER SCHINDLER FINAL LAYOUT DRAWINGS. LIFTING POINTS OR BEAMS SHALL BE VISIBLY MARKED WITH THE SAFE WORKING LOAD.

30.

WHEN INSTALLATION OF TWO RATED HOIST BEAMS PER SCHINDLER REQUIREMENTS PER HOISTWAY IS NOT FEASIBLE, GC SHALL PROVIDE ALTERNATIVE ANCHORAGE METHODS. ALTERNATIVE ANCHORAGES MUST BE CAPABLE OF SUPPORTING AT LEAST 5,000 POUNDS (22.2 KN) PER EMPLOYEE ATTACHED; OR DESIGNED, INSTALLED AND USED UNDER THE SUPERVISION OF QUALIFIED PERSON AS PART OF A COMPLETE PERSONAL FALL PROTECTION SYSTEM, THAT MAINTAINS A SAFETY FACTOR OF AT LEAST TWO, IN ACCORDANCE WITH OSHA STANDARD 1910.140 (C) (13). SCHINDLER WILL VERIFY THE ALTERNATIVE ANCHORAGE POINTS DOCUMENTATION PRIOR TO MOBILIZING TO JOBSITE/PROJECT.

31.

CLASS "ABC" FIRE EXTINGUISHERS IN ELECTRICAL MACHINERY AND CONTROL SPACE. EXTINGUISHERS SHALL BE LOCATED CONVENIENT TO ACCESS DOOR (RULE 8.6.1/8.5).

32.

FURNISH ADEQUATE ON-SITE REFUSE CONTAINERS FOR THE PROPER DISPOSAL OF ELEVATOR PACKAGING MATERIAL. IF ADEQUATE CONTAINERS ARE NOT FURNISHED, DISPOSAL OF PACKAGING MATERIAL SHALL BECOME THE RESPONSIBILITY OF THE OWNER.

33.

TEMPORARY SERVICE: SCHINDLER SHALL BE REIMBURSED FOR ANY LABOR AND MATERIAL THAT IS NOT PART OF THE PERMANENT ELEVATOR INSTALLATION AND THAT IS REQUIRED TO PROVIDE TEMPORARY ELEVATOR SERVICE. SCHINDLER'S TEMPORARY ACCEPTANCE FORM SHALL BE EXECUTED AND THE ELEVATOR INSPECTED BEFORE BEING PLACED INTO TEMPORARY SERVICE. THE COSTS ASSOCIATED WITH THE POWER, OPERATION, MAINTENANCE, AND REHABILITATION OF THE EQUIPMENT AND ANY CONSTRUCTION PERMITS OR FEES REQUIRED BY GOVERNING AUTHORITIES SHALL BE PAID FOR BY OTHERS.

34.

WHERE THERE IS A BLIND HOISTWAY, AN EMERGENCY DOOR SHALL BE INSTALLED AT EVERY THIRD FLOOR, BUT NOT MORE THAN 11M (36FT) FROM SILL TO SILL. THE CLEAR OPENING MUST BE AT LEAST 700MM (28") WIDE AND 2030MM (80") HIGH (RULE 2.11.1.2).

35.

A TEMPORARY WORK PLATFORM IS REQUIRED FOR INSTALLATION OF THE ELEVATOR - UNLESS OTHERWISE DIRECTED BY SCHINDLER. IT IS TO BE CONSTRUCTED AT THE TOP FLOOR OF EACH TRACTION ELEVATOR. IT MUST COMPLY WITH APPLICABLE GOVERNING CODES & REGULATIONS. THE PLATFORM SHALL BE SECURELY FASTENED TO THE BUILDING STRUCTURE. ERECTION, MAINTENANCE, AND REMOVAL ARE BY OTHERS. (REFERENCE SCHINDLER DRAWING TD440)

36.

IN ADDITION TO THE ABOVE, THE FOLLOWING WORK MUST BE COMPLETED BEFORE ELEVATOR(S) ARE PLACED INTO AUTOMATIC OPERATION. (PRIOR TO CODE REQUIRED MUNICIPAL AUTHORITY INSPECTION. REFER TO SCHINDLER ACCEPTANCE INSPECTION STANDARD FORM).

A.

FINISHED CAB FLOORING AND IF APPLICABLE, FITTING OF INTERIOR CAB WALLS AND/OR CEILING.

B.

IF APPLICABLE, SMOKE AND/OR HEAT DETECTORS WITH SIGNALS TO ELEVATOR CONTROLLER(S).

C.

IF APPLICABLE, EMERGENCY POWER GENERATOR AND AUTOMATIC TRANSFER SWITCH WITH CAPACITY TO RUN AT LEAST ONE ELEVATOR AT A TIME.

D.

SEAL ALL PENETRATIONS THROUGH 2-HOUR (OR GREATER) RATED WALLS WITH CODE APPROVED MATERIAL. DRYWALL LINER BEHIND ALL WALL MOUNTED HALL FIXTURES.

E.

ALL RECEPTACLES INSTALLED IN MACHINE/CONTROL ROOMS, MACHINERY SPACES AND PITS MUST HAVE GROUND FAULT CIRCUIT INTERRUPTER PROTECTION (GFCI) (NEC 620 OR CSA 38).

F.

IF APPLICABLE, CONDUIT AND WIRING FOR FIRE ALARM SYSTEM TO EACH ELEVATOR CONTROL IN MACHINE/CONTROL ROOM.

G.

IF APPLICABLE, CONDUIT AND WIRE RUNS FOR EMERGENCY/RESCUE COMMUNICATIONS IN CENTRAL ALARM & CONTROL FACILITY, FIRE CONTROL ROOM, SECURITY DESK, ETC.

H.

IF APPLICABLE, CONDUIT AND WIRE RUNS FOR REMOTE ALARM BELL FROM MACHINE/CONTROL ROOM TO REMOTE LOCATION.

I.

ADEQUATE LIGHTING OF BUILDING CORRIDORS SO THAT ILLUMINATION AT THE LANDING SILL IS MINIMUM 100 LUX (10FC) (RULE 2.11.10.2).

J.

NFPA 72 (FIRE APPARATUS CODE) REQ. 6.15.2.2 REQUIRES THE FIRE CONTROL PANEL RELAYS THAT PROVIDE THE DRY CONTACTS TO OUR CONTROLLER NOT BE LOCATED MORE THAN 3 FEET FROM THE INSPECTION & TEST PANEL JAMB.

CHANGE NOTICES MUST BE RECEIVED AND FULLY EXECUTED PRIOR TO SCHINDLER ELEVATOR COMPANY PERFORMING ANY ADDITIONAL WORK OUTSIDE OF THE SCOPE OF THE BASE CONTRACT. WRITTEN OR VERBAL NOTICES WILL NOT BE ACCEPTED AS A SUBSTITUTE FOR A FULLY EXECUTED CHANGE NOTICE.

SUB	REVISION DESCRIPTION	DATE	APPV.D.	
Schindler Schindler Elevator Corp. 20 Whippany Road Morristown, Tel. +1 www.us.schindler.com				GC PACKAGE WORK BY OTHERS 3300
BUILDING:				
LOCATION:				
OWNER: N/A				
ARCHITECT: N/A				
GEN. CONTRACTOR: N/A				
ENGINEER: ?				
DATE: 08/18/2025				
WBS #	SUB.	CAR	SHEET	
	0##	01	1 OF 6	

YOU AGREE TO INDEMNIFY AND SAVE SCHINDLER HARMLESS AGAINST ANY AND ALL LIABILITY AND COSTS ARISING OUT OF YOUR FAILURE TO CARRY OUT ANY OF THE FOREGOING REQUIREMENTS.

WE INVITE YOU TO VISIT OUR WEB SITE: <http://www.us.schindler.com>

GENERAL	
CAR NUMBER	01
ELEVATOR TYPE	GENERAL PURPOSE
CAPACITY / LOADING CLASS	3500 lbs [1590 KG] / CLASS A
SPEED (VKN)	100 fpm [0,5 m/s]
CONTROL SYSTEM	NX100
CONTROL TYPE	SELECTIVE COLLECTIVE AUTOMATIC
DRIVE SYSTEM	VARIODOYN
MACHINE VOLTAGE	480
DRIVE TYPE	VAF023_480
SEISMIC CATEGORY	A
LOCAL REGULATION CODE	TX1, A17.1 - 2016
LOCAL BUILDING CODE	IBC 2015
NFPA13 CODE	N/A
FIREFIGHTER CAR	NO
STRETCHER CAR	YES**
CP NUMBER	N/A
HOISTWAY	
MACHINE/CWT LOCATION	ON RAIL IN OVERHEAD
OVERHEAD (HSK)	12'-7" [3835 mm]
TRAVEL (HQ)	15' [4572 mm]
PIT DEPTH (HSG)	5' [1524 mm]
HOISTWAY WIDTH (BS)	8'-6" [2591 mm]
HOISTWAY DEPTH (TS)	6'-11" [2108 mm]
ENTRANCES (OPENINGS)	2 (2 FRONT / 0 REAR)
QUANTITY OF LANDINGS	2
PIT SET DRILLING	YES
TRACTION	
MACHINE TYPE	FMB130-NN-4D560
MACHINE HORSEPOWER	6.95 (NOT FOR SIZING)
BRAKE ASSEMBLY TYPE	FMB130-NN-4D560
BRAKE MODEL	LEROY SOMER MAGNETIC DISK BRAKE
BRAKE QUANTITY/TYPE	2 MAGNETIC DISK BRAKES
DRIVE/CAR SHEAVE DIA	3.4" (87 MM)
STM BELT TYPE	STM-PV30 (FIRE RATED)
STM QTY	4
STM LENGTH (EACH)	76' [23.2 M]
STM TRIP COUNT LIMIT	30
ROPING	2:1
ENTRANCES	
LANDING DOOR TYPE-FRONT	2-SPD SIDE OPENING LEFT HAND (T2R)
LANDING DOOR TYPE-REAR	N/A
DOOR WIDTH (BT)	3'-6" [1067 mm]
DOOR HEIGHT (HT)	7' [2134 mm]
CAB HEIGHT (HK)	7'-9 1/8" [2366 mm]
LANDING DOOR LOCK TYPE	FERMATOR
LANDING DOOR FIRE RATING	UL 10B1.5 HOURS
DOOR OPERATOR TYPE	FERMATOR COMPACT
DOOR CLUTCH TYPE	FERMATOR COMPACT

CAR ENCLOSURE MEETS THE EQUIVALENT DEFLECTION AND ALLOWABLE STRESS REQUIREMENTS OF 2.15.10 AND 2.15.11

FIELD NOTES:

- MEETS ASME A17.1, ADA AND LOCAL CODES.
- STM TWIST 180 DEGREES BETWEEN CAR AND MACHINE.
- PER ASME A17.1-2016/CSA B44-07 WITH ADDENDAS A-2008 AND B-2009 AND EDITION 2010 INCLUDES COMMUNICATIONS FAILURE INDICATOR TO BE LOCATED IN VICINITY OF PHASE 1 FIRE RECALL SWITCH.
- THIS CONTRACT COMPLIES WITH ASME A17.1-2007/CSA B44-07 WITH ADDENDAS A-2008 AND B-2009 AND EDITION 2010 AND WHERE APPLICABLE INCLUDES EXCEPTION TO THOSE POINTS COVERED UNDER THE ACCOMPANYING VARIANCE DOCUMENTS RELATED TO THE SUSPENSION SYSTEM AND GOVERNOR ROPES THAT CONFORM TO THE LATTER 2010 EDITION AND TO ASME A17.6-2010.

****ACCOMMODATES A MAXIMUM STRETCHER SIZE OF 84" x 24" [2134 x 610]**

SAFETY ELEMENTS & GUIDE RAILS	
CAR NUMBER	01
CAR SAFETY TYPE	SCHINDLER-RF1
CAR GOVERNOR TYPE	SA GBP 202
CAR GOV. ROPE LENGTH	66.00' [20 m]
CAR GOV. ROPE TYPE	6MM DIA.
CAR GUIDERAILS	12 lbs/ft (T127-1/B)
CWT GUIDERAILS	6 lbs/ft (T75)
CAR GUIDESHOE TYPE	SLIDING
CWT GUIDESHOE TYPE	SLIDING
CAR BUFFER TYPE	SPRING (E1)
CAR BUFFER QTY	2
CAR BUFFER STROKE	1 9/16" [40 mm]
CAR BUFFER SPRING OUTER DIA. / LENGTH	4.1 [104.7] / 6.8 [173]
CAR RUNBY	6" [152 mm]
CWT BUFFER TYPE	SPRING (D3-01)
CWT BUFFER QTY	1
CWT BUFFER STROKE	2 1/2" [64 mm]
CWT BUFFER SPRING OUTER DIA. / LENGTH	5.5 [139.7] / 9.06 [230.1]
CWT RUNBY	6" [152 mm]

ELECTRICAL DATA	
MAIN POWER SUPPLY	480V; 3 PHASE; 60 Hz
EMERGENCY POWER OPERATION	NO
BATTERY BACKUP (AUTO EVAC)	YES
AUTOTRANSFORMER	NO


SYSTEM WEIGHTS	
CAR NET AREA	37.78 ft2 [3.51 m2]
CAR FLOOR THICKNESS (HKZ)	3/8" [10 mm]
CAR ADDITIONAL WEIGHT	0 LBS [0 KG]
CAR WEIGHT	2342 LBS [1062 KG]
MASS ACTING ON SAFETIES (GKU)	5849 LBS [2653 KG]
CWT WEIGHT	4097 LBS [1858 KG]
CWT PERCENTAGE	50%
FLOOR WEIGHT BY OTHERS	150 LBS [68 KG]

CONTROL OPTIONS	
EMERGENCY SERVICE / CODE BLUE	NO
HALL SECURITY	NONE
CAB SECURITY	CAR CARD READER PROVISIONS
VIP SERVICE	NO
WATER DETECTION IN PIT	NO
TEXT/VIDEO COMMUNICATION	NO
LOBBY VISION INTERFACE	NO
STATUS (FIREFIGHTER) PANEL	NO
ECP WIRING DISTANCE	N/A


ACRONYM	DEFINITION
BGS	DISTANCE BETWEEN COUNTERWEIGHT GUIDE RAILS
BIA	BUFFER IMPACT ASSEMBLY
BK	CAR WIDTH (INSIDE)
BKE	CAR ENTRANCE CLEAR WIDTH
BKF1	CAB INSIDE WALL WIDTH (FRONT LEFT)
BKF2	CAB INSIDE WALL WIDTH (FRONT RIGHT)
BKF3	CAB INSIDE WALL WIDTH (REAR RIGHT)
BKF4	CAB INSIDE WALL WIDTH (REAR LEFT)
BKS	DISTANCE BETWEEN CAR GUIDE RAILS
CCL1	CAR C/L TO MACHINE/CWT SIDE WALL
CCL2	CAR C/L TO LONE RAIL SIDE WALL
CCU	CAR CONTROL UNIT
CIN	CAR LANTERN
COP	CAR OPERATING PANEL
DCL	DOOR C/L
F	FORCE ON GUIDE SHOE IN DIRECTION OF GUIDE RAIL AXIS ON CAR SIDE OR CWT SIDE
FF1	REFER TO F FOR ACTING FORCES ON CAR SIDE
FF1g	REFER TO F FOR ACTING FORCES ON CWT SIDE
FF2	REFER TO P FOR ACTING FORCES ON CAR SIDE
FF2g	REFER TO P FOR ACTING FORCES ON CWT SIDE
F11	FORCE OF LONE CAR RAIL ON HOISTWAY PIT
F9	FORCE OF CAR BUFFER ON HOISTWAY PIT
F40	FORCE OF CWT BUFFER ON HOISTWAY PIT
F12	FORCE OF CWT-SIDE CAR RAIL ON HOISTWAY PIT
F14	FORCE OF CWT RAIL ON FRONT OF HOISTWAY PIT
F13	FORCE OF CWT RAIL ON REAR OF HOISTWAY PIT
HE	FLOOR TO FLOOR DISTANCE
HF	DISTANCE BETWEEN GUIDE RAIL BRACKETS
HGU	CAR FRAME BOTTOM HEIGHT
HK	CAR HEIGHT

ACRONYM	DEFINITION
HKA	CAR TOE GUARD HEIGHT
HKB	PLATFORM & FLOORING THICKNESS
HP CAR	FULL CAR BUFFER HEIGHT
HP CWT	FULL CWT BUFFER HEIGHT
HPE CAR	HEIGHT OF COMPRESSED CAR BUFFER
HPE CWT	HEIGHT OF COMPRESSED CWT BUFFER
HSS1	HEIGHT OF CAR PLINTH
HSS2	HEIGHT OF CWT PLINTH
JH1	AUXILIARY DISCONNECT
JH	MACHINE DISCONNECT
JHL	CAR SUPPLY DISCONNECT
LIN	HALL LANTERN
LOP	HALL PUSH BUTTON
LDU	LANDING DOOR UNIT, PROVIDES INSPECTION AND TEST PANEL ACCESS
LF CAR	CAR RAIL LENGTH
LF CWT	CWT RAIL LENGTH
P	FORCE ON GUIDE SHOE PERPENDICULAR TO GUIDE RAIL AXIS ON CAR OR CWT SIDE
RO	ROUGH OPENING
SF1	LEFT HW WALL TO BASE OF CAR RAIL DISTANCE
SF2	RIGHT HW WALL TO BASE OF CAR RAIL DISTANCE
SG	HW WALL TO CWT C/L
SKO	OVER-TRAVEL OF CAR ABOVE
SKS	HALF-GRAVITY STOPPING DISTANCE
SKU	OVER-TRAVEL OF CAR CAR BELOW
STM	SUSPENSION TRACTION MEDIA
TA	AUTOTRANSFORMER 20KVA
TAS	CONTROL TRANSFORMER 1KVA
TCRR	TOP OF CAR RAIL
TCWR	TOP OF COUNTERWEIGHT RAIL
TG	COUNTERWEIGHT DEPTH
TK	CAR DEPTH (INSIDE)
TKA	CAR SILL TO INSIDE CAR WALL
TKS	RUNNING CLEARANCE
TKSW1	CAR C/L TO FRONT HW WALL DISTANCE
TKSW2	CAR C/L TO REAR HW WALL DISTANCE
TSU	TRANSFER SWITCH UNIT
TSW	ENTRANCE SILL DEPTH
XCW	CWT C/L TO CAR GUIDE RAIL BASE DISTANCE


SUB	REVISION DESCRIPTION		DATE	APPV'D.	
 Schindler Schindler Elevator Corp. 20 Whippany Road Morristown, [REDACTED] Tel. +1 [REDACTED] www.us.schindler.com					GC PACKAGE SPECIFICATIONS & DATA
BUILDING:	[REDACTED]				
LOCATION:	[REDACTED]				
OWNER:	N/A				
ARCHITECT:	N/A				
GEN. CONTRACTOR:	N/A				
ENGINEER:	?				
DATE:	08/18/2025				
WBS #	SUB.	CAR	SHEET		
	0##	01	2 OF 6		
					3300

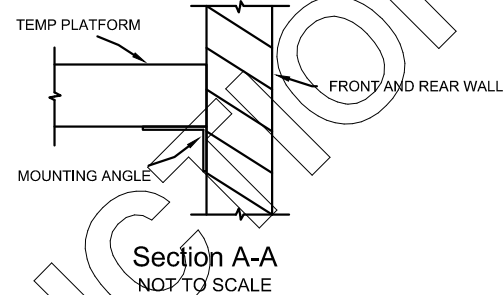

Scale: 1/2"=1'0"
SEE NOTES #1-6

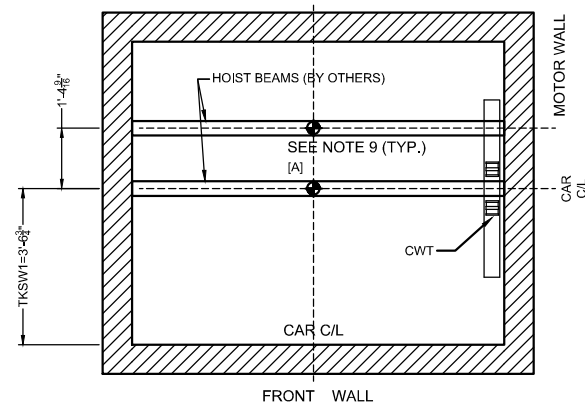


OVERHEAD HOIST BEAMS
Scale: 1/2"=1'0"




VERTICAL LOADS CAR 01					
NOTE: F9 DOES NOT OCCUR SIMULTANEOUSLY WITH F11 & F12					
BUFFER IMPACT		GUIDE RAILS IMPACT			
		RAIL LOADS INCLUDE SAFETY APPLICATION & EQUIPMENT WEIGHT			
F9	F10	F11	F12	F13	F14
9073 lbf	12938 lbf	18144 lbf	22417 lbf	3677 lbf	3677 lbf
40.4 kN	57.5 kN	80.7 kN	99.7 kN	16.4 kN	16.4 kN

- # NOTES:
1. TEMPORARY PLATFORM TO BE CONSTRUCTED OF 2 x 10 DOUGLAS FIR GRADE 2. REQUIREMENT FOR THE TOP LANDING PLATFORM AND ITS REMOVAL SHALL BE COORDINATED WITH THE SCHINDLER SUPERINTENDENT.
 2. PLATFORM TO BE COVERED BY 2 LAYERS OF 5/8" [16] PLYWOOD DECKING 5/8" [16] THICK CDX GRADE. WORK PLATFORM RATED TO HANDLE 1000 Lbs [454 kg].
 3. METAL BEARING ANGLES 6" x 6" x 3/8" [152 x 152 x 10] TO BE FIXED TO BUILDING WALLS, FRONT AND BACK, WITH PLATFORM AFFIXED TO TOP OF BEARING ANGLE. SHALL BE EQUAL OR GREATER THAN THE WIDTH OF THE PLATFORM. METAL BEARING ANGLES RATED TO HANDLE 1500 lbs [680 kg]. PLATFORM DESIGNED & PROVIDED BY OTHERS. SEE SECTION A-A
 4. GUIDE RAILS INCLUDE SAFETIES APPLICATION, GOVERNOR LOAD AND EQUIPMENT ON RAILS.
 5. PLATFORM TO BE LEVEL WITH TOP FLOOR OPENING WITH EASY REACH OF HOISTBEAMS FOR ATTACHMENT OF FALL ARREST LIFELINES, LANYARDS, OR DECELERATION DEVICES.
 6. PLATFORM TO BE BUILT & REMOVED BY OTHERS. FRONT WALL AT TOP LANDING TO NOT BE INSTALLED UNTIL THIS PLATFORM IS REMOVED.
 7. SUMP PIT IN ELEVATOR PITS, WHERE PROVIDED, SHALL COMPLY WITH THE APPLICABLE PLUMBING CODE, AND THEY SHALL BE PROVIDED WITH A POSITIVE MEANS TO PREVENT WATER, GASES AND ODORS FROM ENTERING THE HOISTWAY. SUMPS AND SUMP PUMPS IN PITS, WHERE PROVIDED, SHALL BE COVERED. THE COVER SHALL BE SECURED AND LEVEL WITH THE PIT FLOOR PER APPLICABLE A17.1 EDITION AND SHOULD BE LOCATED TO CLEAR ELEVATOR EQUIPMENT (CANNOT BE CONNECTED DIRECTLY TO STORM DRAIN OR SEWER). PLACEMENT OF SUMP PUMP SHALL NOT IMPEDE ON DESIGNATED REFUGE SPACE. SUMP PITS INCLUDING PUMPS AND PIPES MUST BE LOCATED AT A MINIMUM OF 12" FROM RAIL FOOT PRINT (REFER TO HATCH PLAN). ONLY ONE SUMP PUMP REQUIRED IF HOISTWAYS ARE OPEN TO EACH OTHER. COORDINATE SUMP LOCATION WITH SCHINDLER SUPERINTENDENT.
 8. PIT LIGHT ("LT") & GFCI BY OTHERS. LOCATE ON REAR WALL NO LESS THAN 32" [813] BELOW BOTTOM LANDING.
 9. A) GC TO PROVIDE AND INSTALL STEEL I-BEAMS AS SHOWN IN THE OVERHEAD HOIST BEAMS DETAIL. EACH BEAM SHALL BE CAPABLE OF WITHSTANDING A MINIMUM LIVE LOAD OF 7500 lbs [3402 kg] PLACED ANYWHERE ALONG THE SPAN.
B) BEAMS SHALL BE MARKED WITH THE SAFE WORKING LOAD.

SUB	REVISION DESCRIPTION			DATE	APPVD.				
 Schindler Elevator Corp. 20 Whippary Road Morristown, [REDACTED] Tel. +1 [REDACTED] www.us.schindler.com Schindler					GC PACKAGE PLAN VIEWS				
						BUILDING: [REDACTED]			
						LOCATION: [REDACTED]			
						OWNER: N/A			
						ARCHITECT: N/A			
GEN. CONTRACTOR: N/A				3300					
ENGINEER: ?									
DATE: 08/18/2025									
WBS #	SUB.	CAR	SHEET						
	0##	01	3 OF 6						


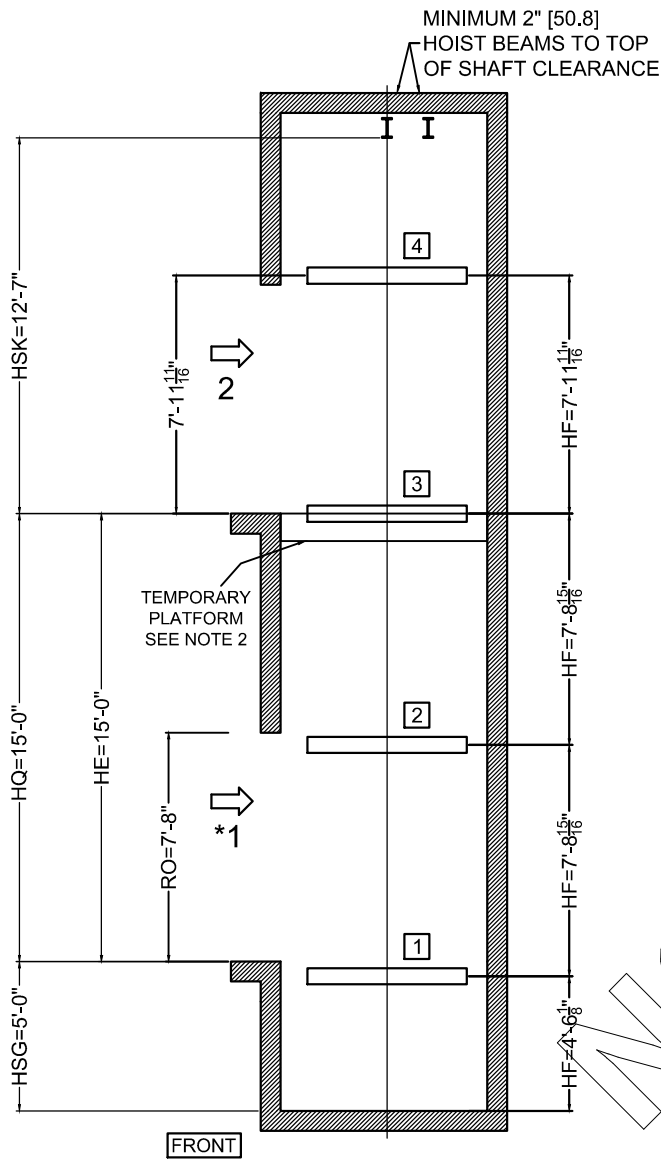


ELEVATION DETAIL CAR 01

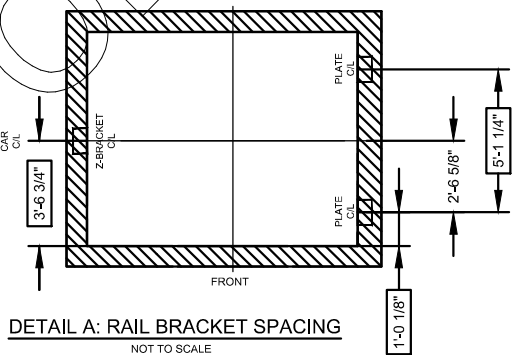

BRACKET INTERFACE WALL CONSTRUCTION TYPE CAR 01	
FROM OUTSIDE SHAFT LOOKING IN	TYPE
LEFT WALL	CONCRETE*
RIGHT WALL	CONCRETE*




*INSERTS NOT PROVIDED.

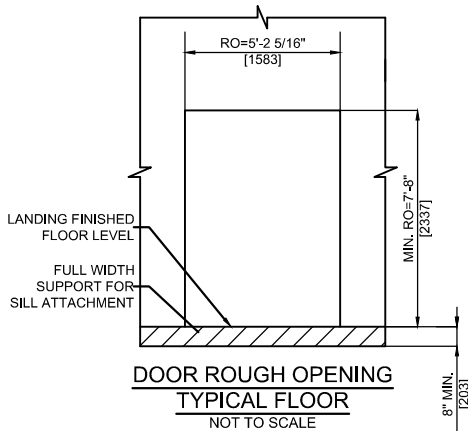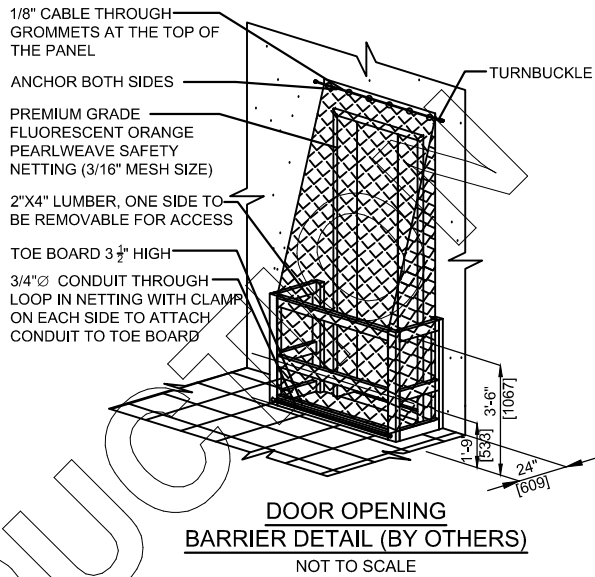

RAIL STACK LEGEND			
SYMBOL	DESCRIPTION		
#	GUIDE RAIL BRACKET		
#	OPENING		
F&P CAR RAIL LOADS		F&P CWT RAIL LOADS	
F (FF1)	P (FF2)	F (FF1)	P (FF2)
364 lbf	173 lbf	72 lbf	7 lbf
1619 N	770 N	320 N	31 N

- NOTES:
1. MAXIMUM RAIL BRACKET SPAN ALLOWED IS 10'-9 15/16" [3300]. MAXIMUM SPACING BETWEEN BRACKETS FROM L BRACKET TO LAST OMEGA BRACKET OR FROM OVERHEAD Z BRACKET TO Z BRACKET BELOW IS 10'-9 15/16" [3300].
 2. TEMPORARY PLATFORM WITH CORRESPONDING BEARING SUPPORTS TO BE PROVIDED BY OTHERS.
 3. SMOKE VENT LOCATED IN OVERHEAD PER APPLICABLE A17.1 EDITION.
 4. OUT OF LEVEL OF PIT FLOOR NOT TO EXCEED +0.5" [+12].
 5. A BUILDING SUPPORT (PROVIDED BY THE GC) IS REQUIRED AT THE SPECIFIED ELEVATION FOR ATTACHMENT OF THE ELEVATOR RAIL BRACKETS TO THE BUILDING. THE MAXIMUM DEFLECTION OF THE BRACKET SUPPORT SHOULD NOT EXCEED .0625" [1.5] FOR NON-SEISMIC LOCATIONS OR 0.125" [3] FOR SEISMIC LOCATIONS.
 6. ALL DIMENSIONS ARE FROM FINAL FINISHED FLOOR.
 7. HATCH WIDTH, HATCH DEPTH, PIT DEPTH AND OVERHEAD TO BE +1"/-0"
 8. HATCH TO BE PLUMB WITHIN 1" TOP TO BOTTOM

SUB		REVISION DESCRIPTION	DATE	APPVD.
 Schindler Elevator Corp. 20 Whippany Road Morristown, NJ Tel. +1 (973) 382-1000 www.us.schindler.com				
BUILDING:				
LOCATION:				
OWNER:		N/A		
ARCHITECT:		N/A		
GEN. CONTRACTOR:		N/A		
ENGINEER:		?		
DATE:		08/18/2025		
WBS #		SUB.	CAR	SHEET
		0##	01	4 OF 6
3300				

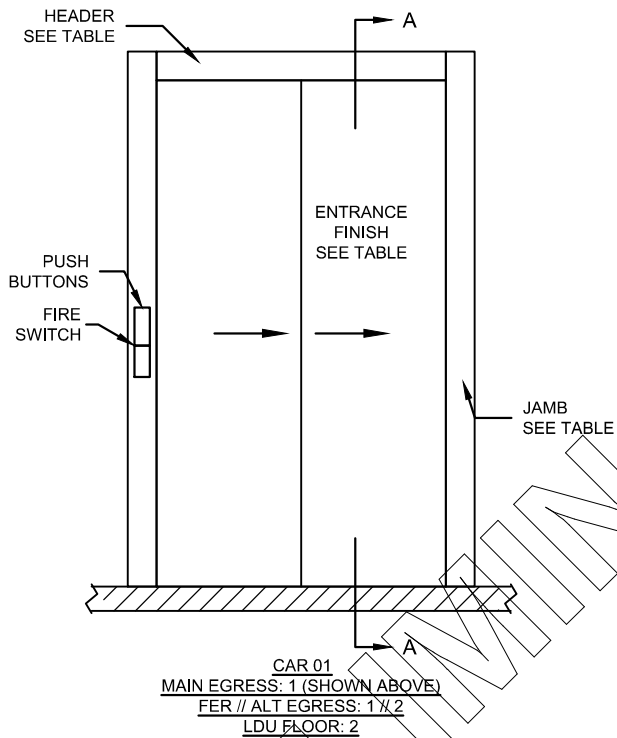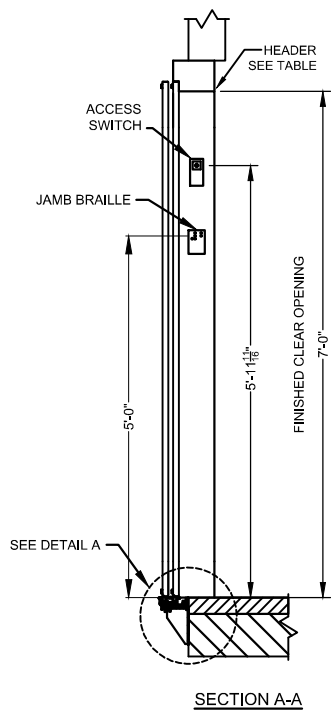

NOTES:

1. HOISTWAY WALLS TO HAVE A FIRE ENDURANCE RATING NOT LESS THAN REQUIRED BY APPLICABLE A17.1 EDITION.
2. FURNISHING, INSTALLING, AND MAINTAINING THE REQUIRED FIRE RATING OF ELEVATOR HOISTWAY WALLS, INCLUDING THE PENETRATION OF FIRE WALL BY ELEVATOR FIXTURE BOXES, IS NOT THE RESPONSIBILITY OF ELEVATOR CONTRACTOR.
3. THE INTERFACE OF HOISTWAY WALL WITH THE HOISTWAY ENTRANCE ASSEMBLY SHALL BE IN STRICT COMPLIANCE WITH THE CONTRACTOR'S REQUIREMENTS IN ORDER TO RETAIN FIRE RATINGS & LABEL VALIDITY OF ELEVATOR HOISTWAY DOORS AND FRAMES.
4. FILLING AND GROUTING AS REQUIRED (BY OTHERS).
5. WHEN WALL MOUNTED FIXTURES, SUPPORT FOR FIXTURE BOXES AS REQUIRED (BY OTHERS).
6. WALL THICKNESS MUST BE MAINTAINED FOR PROPER INSTALLATION OF ENTRANCES.
7. DOOR FIRE RATING 1.5 HR.
8. TOTAL HORIZONTAL FORCE OF 1125 LBF IS IMPOSED ON THE BUILDING STRUCTURE THROUGH ALL THE FIXATION POINTS PER ENTRANCE. REFER TO APPLICABLE A17.1 EDITION.
9. REFER TO FIXTURES SHEET FOR LOCATION OF ALL FIXTURES.
10. FOR CONCRETE WALL CONSTRUCTION, ADDITIONAL 3/4" TOLERANCE IS ADDED TO THE JAMB.



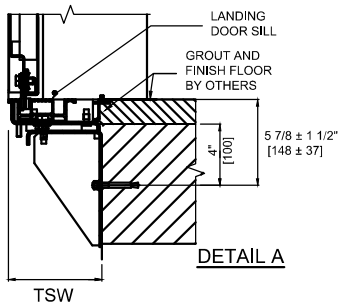


TABLE OF ENTRANCE DETAILS CAR 01										
OPENING		WALL THICKNESS (WT)	CONSTRUCTION		ENTRANCE SILL MATERIAL	JAMB FINISH (14 GA. STL.)/ DOOR FINISH (18 GA. STL.)	DOOR PANEL WEIGHT	JAMB		
FLOOR	TYPE		SILL INTERFACE	WALL INTERFACE				HEADER REVEAL	LEFT REVEAL	RIGHT REVEAL
*1	FRONT	3 1/8" MIN	CONCRETE	CONCRETE	ALUMINUM	#4 STAINLESS STEEL	144.4 LBS [65.5 KG]	4 3/4" [121]	4 3/4" [121]	4 3/4" [121]
2	FRONT	3 1/8" MIN	CONCRETE	CONCRETE	ALUMINUM	#4 STAINLESS STEEL	144.4 LBS [65.5 KG]	4 3/4" [121]	4 3/4" [121]	4 3/4" [121]


SUB		REVISION DESCRIPTION		DATE	APPVD.
BUILDING:		LOCATION:		OWNER:	
ARCHITECT:		GEN. CONTRACTOR:		ENGINEER:	
DATE:		WBS #		SUB.	CAR
0##		01		SHEET	
5 OF 6		3300		ENTRANCES	

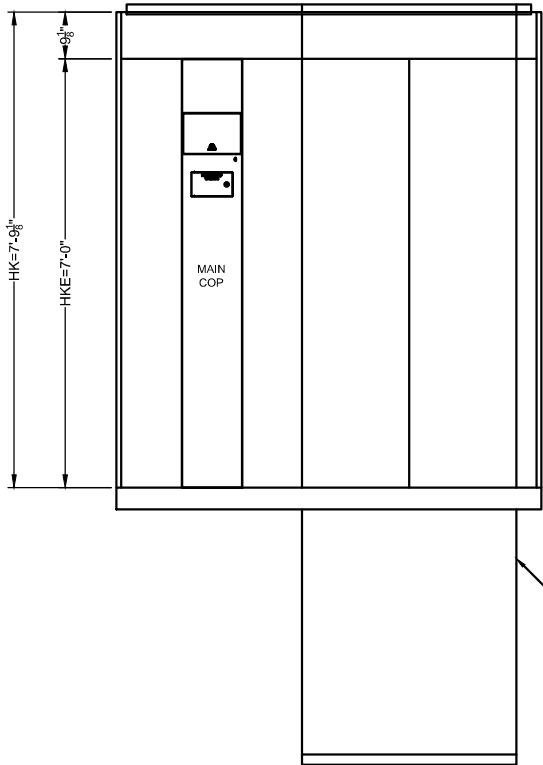


FRONT ELEVATION

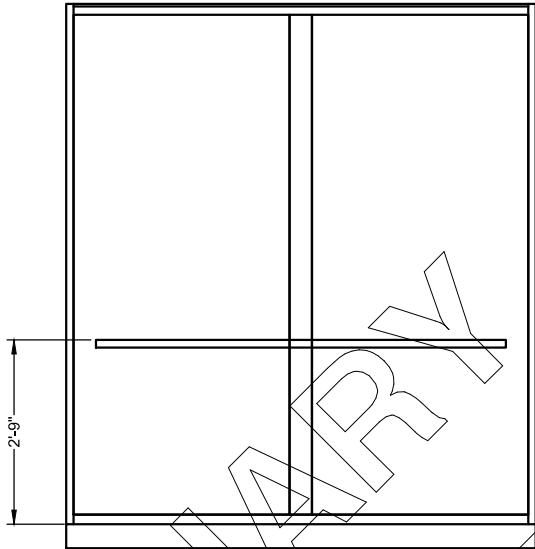


REAR ELEVATION

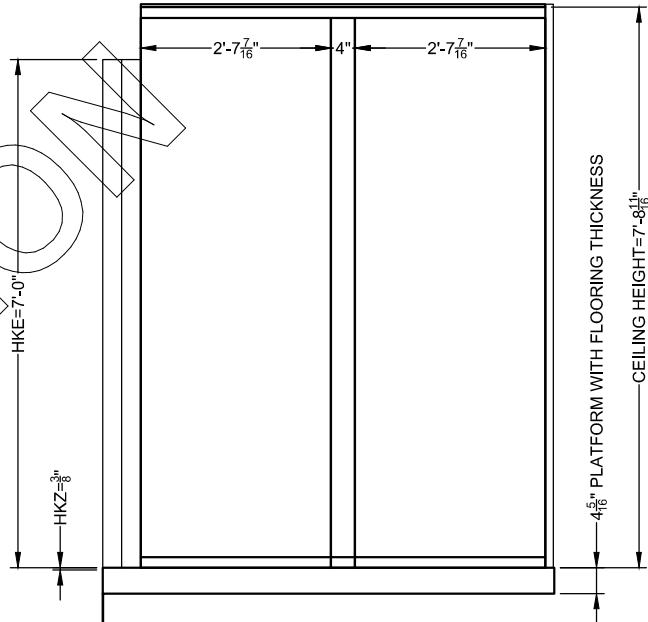

SIDE ELEVATION

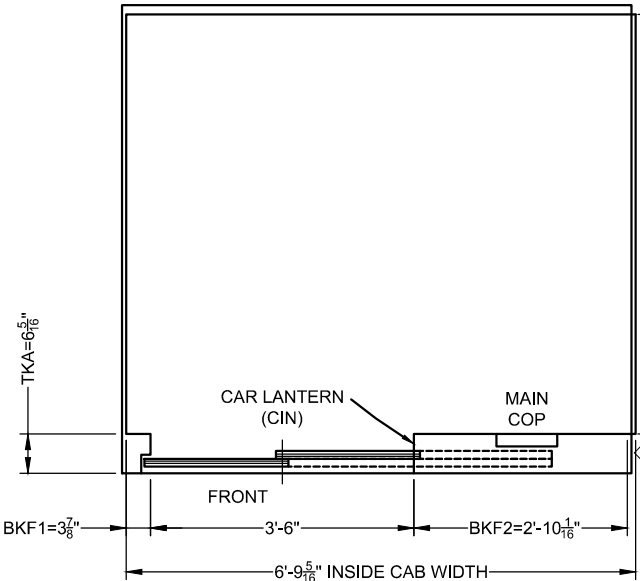

CAR PLAN

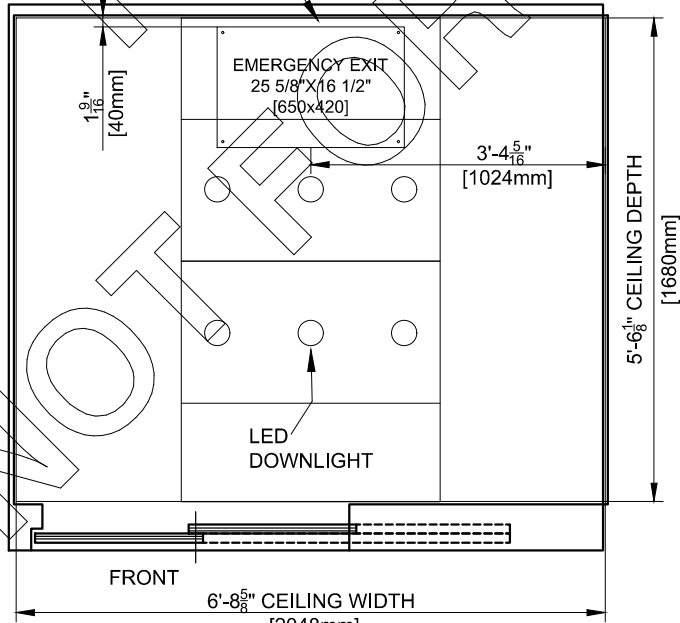

CEILING PLAN

CAR FRONT		OPTIONS	
CAR FRONT DECORATION	#4 STAINLESS STEEL	CAR FAN TYPE	1 SPEED
CAR DOOR DECORATION	#4 STAINLESS STEEL	CAR LANTERN	PROVIDED
CAR DOOR PANEL WEIGHT	150.1 LBS [68.1 KG]	HANDRAIL LOCATION	REAR
COP FACEPLATE MATERIAL	STEEL	HANDRAIL TYPE	RECTANGULAR(STRAIGHT)
CAR POSITION INDICATOR	IN MAIN COP	HANDRAIL FINISH	BRUSHED ALUMINUM
SILL TYPE	ALUMINUM	TELEPHONE	HANDS-FREE ADA
LIGHT CURTAIN TYPE	STATIC LIGHT CURTAIN	FLOOR	
CAR WALLS		FLOOR RECESS	3/8" [10]
SIDE WALL TYPE	APPLIED(LAMINATE)	FLOOR TYPE	BY OTHERS
SIDE WALL FINISH	GC TO ADVISE	CEILING	
REAR WALL	APPLIED(LAMINATE)	LED DOWN LIGHT - ROUND SPOTS	
REAR WALL FINISH	GC TO ADVISE	#4 STAINLESS STEEL	
CEILING		AUTOMATIC ON/OFF	
CEILING TYPE	LED DOWN LIGHT - ROUND SPOTS		
CEILING FINISH	#4 STAINLESS STEEL		
CAR LIGHTING TYPE	AUTOMATIC ON/OFF		

SUB				REVISION DESCRIPTION	DATE	APPVD.
Schindler				Schindler Elevator Corp. 20 Whippany Road Morristown, NJ 07960 Tel. +1 973 382 7000 www.us.schindler.com		
BUILDING:						
LOCATION:						
OWNER:				N/A		
ARCHITECT:				N/A		
GEN. CONTRACTOR:				N/A		
ENGINEER:				?		
DATE:				08/18/2025		
WBS #				SUB.	CAR	SHEET
				0##	01	6 OF 6
